DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

Sheet ____ of ____
PROPERTY ID #: _____
COUNTY: _____

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

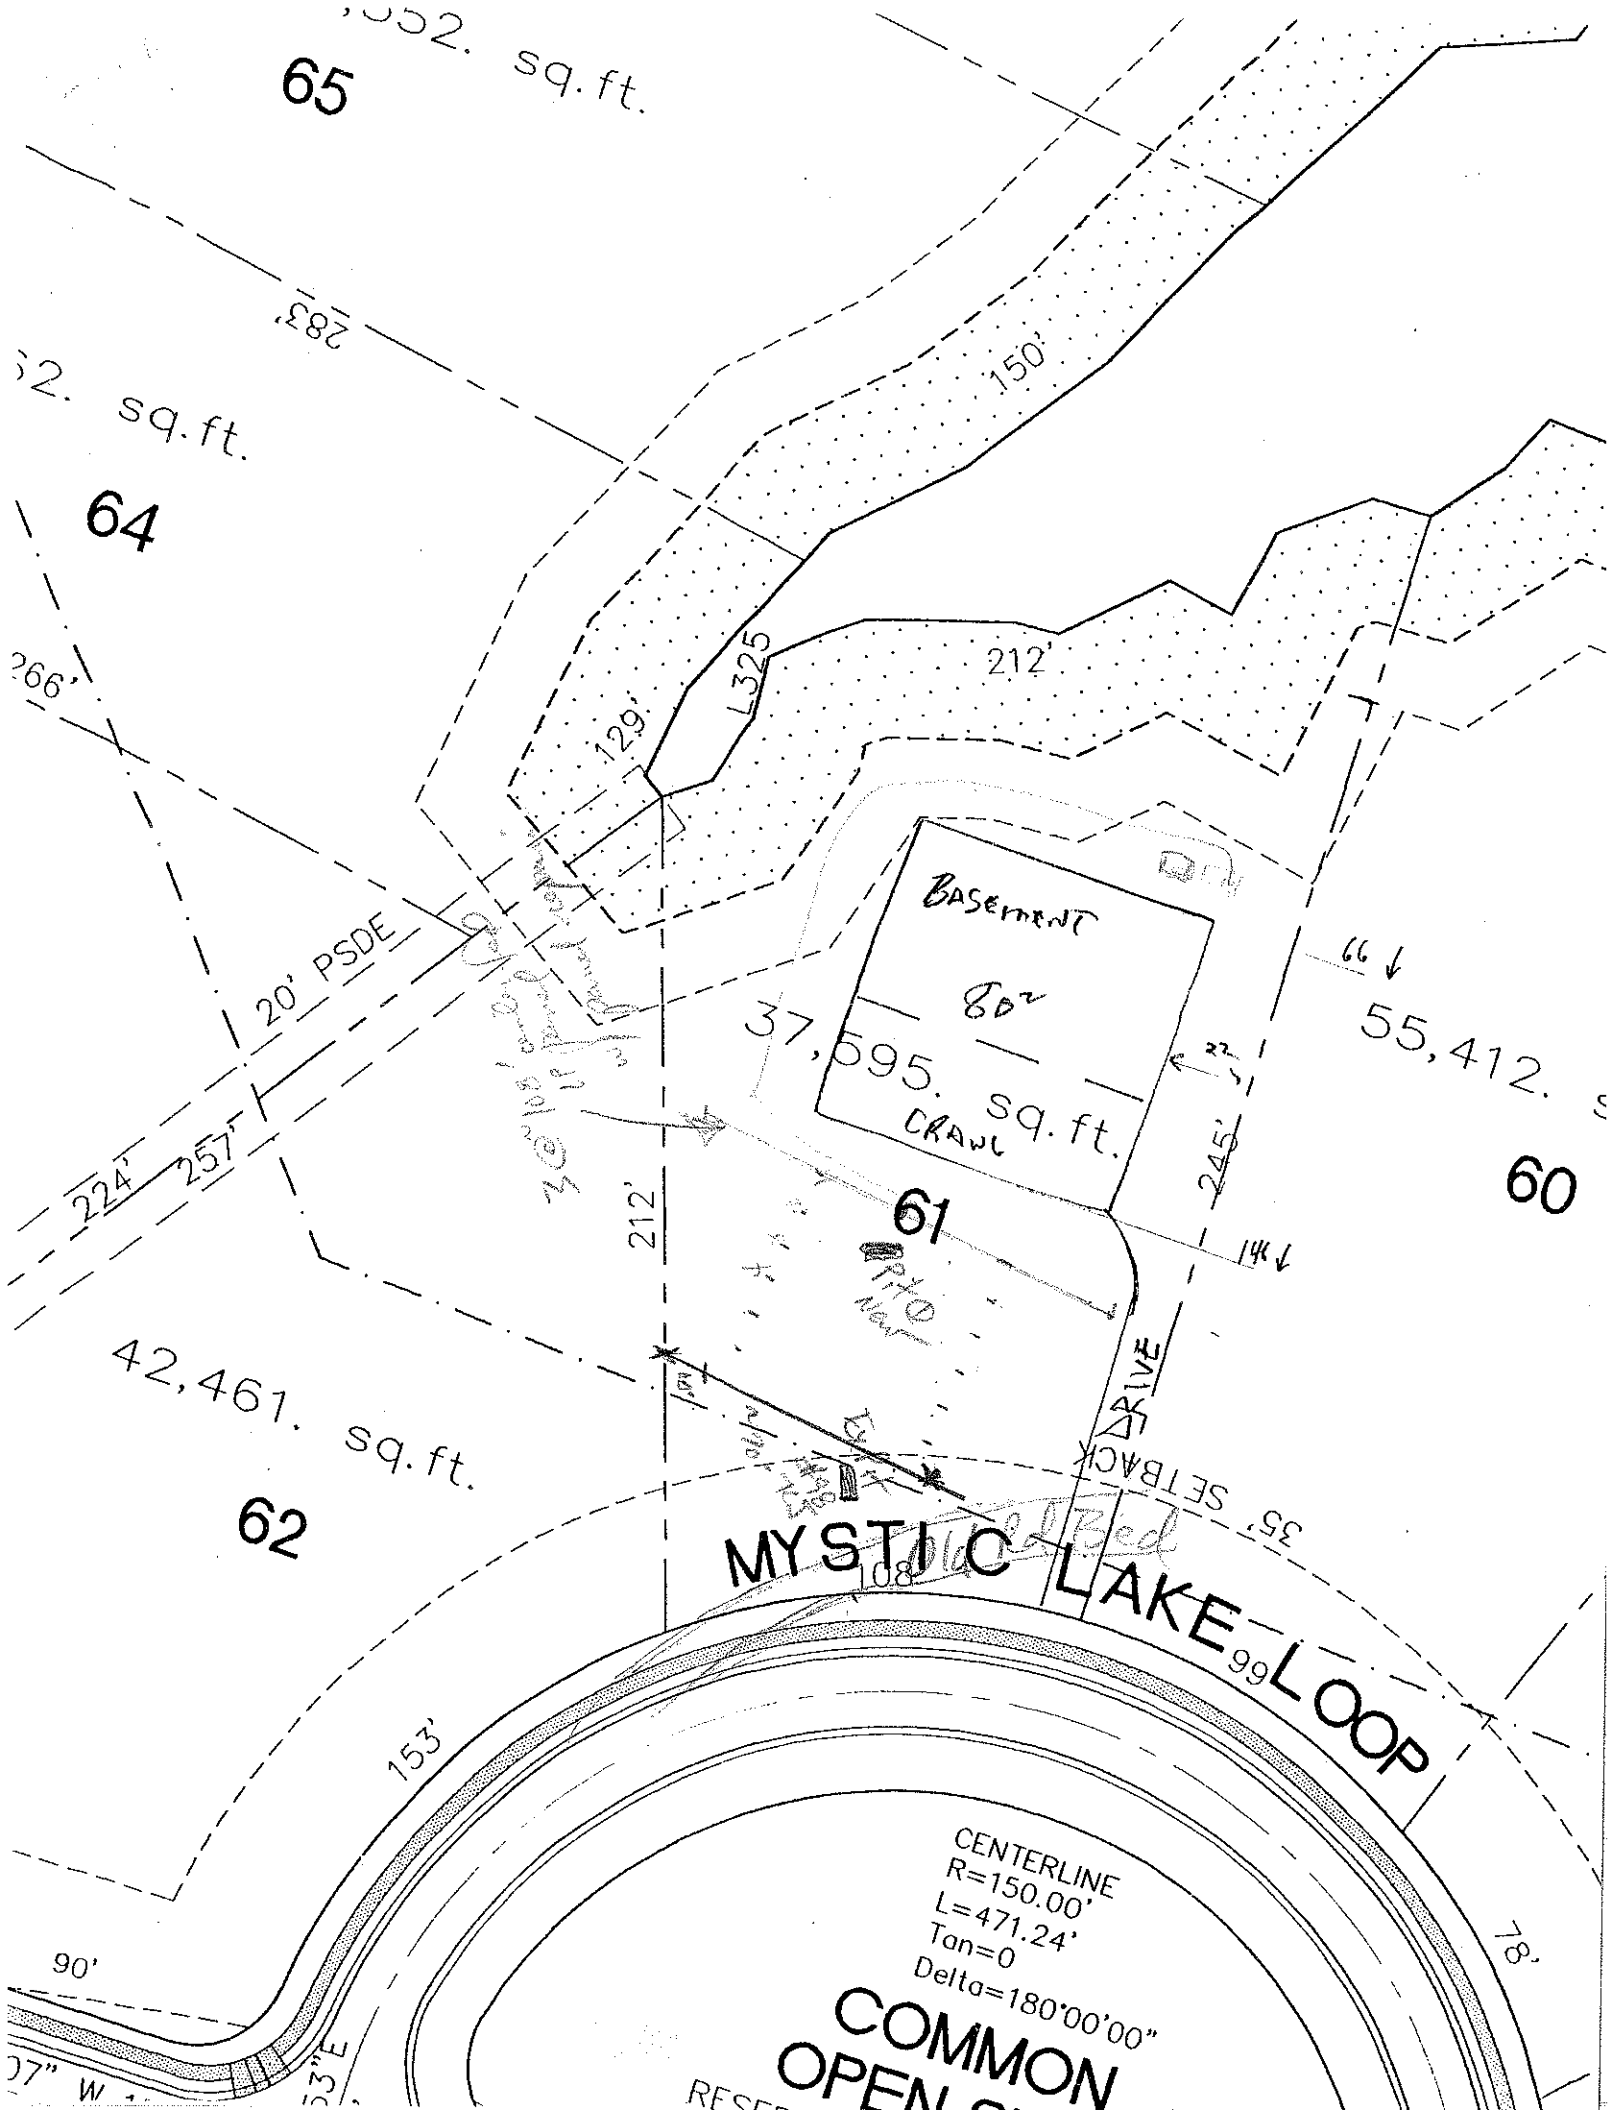
OWNER: CLT APPLICANT: _____
ADDRESS: _____ APPLICATION DATE: _____ DATE EVALUATED: 4-21-98
PROPOSED FACILITY: _____ PROPOSED DESIGN FLOW (.1949): _____ PROPERTY SIZE: _____
LOCATION OF SITE: Lot 61 The Fonta PROPERTY RECORDED: _____
WATER SUPPLY: ☐ Private ☐ Public ☐ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☐ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☐ Sewage ☐ Industrial Process ☐ Mixed

Now Lot 60

PROFILE #	.1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LTAR
1		0-5	sa sl						PS .3
		5-23	sa sl						
		23-50	m-wksab gr sl						
2		0-26	wksab gr sl						PS .25
		26-60	mwksab sl						
			few coarse fragments						
3									
4									

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)		
System Type(s)		
Site LTAR		

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): _____
EVALUATED BY: _____
OTHER(S) PRESENT: _____


65
64
61
62
60
283'
150'
129'
L325
212'
266'
20' PSDE
224'
257'
212'
245'
66'
BASEMENT
80'
37,595. sq. ft.
CRAWL
55,412.
42,461. sq. ft.
DRIVE
35' SETBACK
MYSTIC LAKE LOOP
99
108
153'
90'
78'
CENTERLINE
R=150.00'
L=471.24'
Tan=0
Delta=180°00'00"
COMMON
