IREDELL COUNTY HEATLH DEPARTMENT

PAGE 2: *SITE PLAN WORKSHEET*

SEE THE SAMPLE SITE PLAN BELOW. INCOMPLETE SITE PLANS WILL BE RETURNED TO YOU FOR COMPLETION AND MAY RESULT IN A DELAY IN THE ISSUANCE OF YOUR SEPTIC SYSTEM PERMIT!!!

Place an (X) beside each item as you complete the site plan:

- X Property Line measurements are clearly identified...
- X All proposed structures are indicated...
  SHOW: proposed house or business footprint, wells, water lines, patios, pools and decks, and any other item that will occupy space on the site
- X Front and side setbacks from property line...
- X Preferred driveway location and configuration, preferred well location...
- X Area you prefer your septic system to be placed...
- X North arrow, or other sufficient indicator of direction...


Circle N/A on the following if appropriate:

- ____ Location of septic systems and wells within 100' of your property... N/A
- ____ Location of easements and rights of ways on your property... N/A
- ____ Location of any designated wetlands on the property... N/A

Signature: Tony Jacobs ARP
Property owner or owner's legal representative signature (SIGNATURE REQUIRED)

10-5-07
DATE


USE THIS SPACE TO DRAW YOUR SITE PLAN

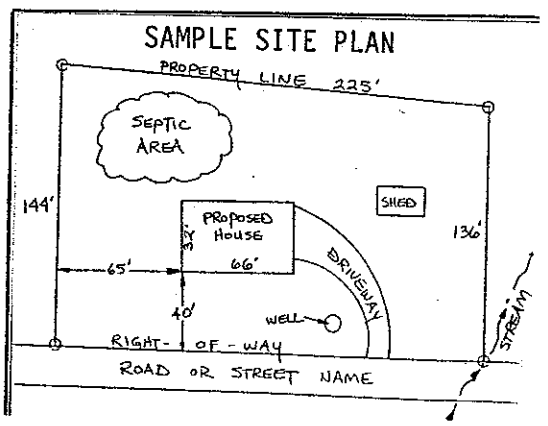

DAS DON ALLEN & ASSOCIATES, P. A.
"Since 1971"
Commercial * Residential * Mortgage Surveys * Multi-Family
Construction Staking * Subdivision Design * Topographical
111-B Raceway Drive * Mooresville * NC * 28117
(704) 664-7029 (704) 664-8041 Fax


I, certify that this map was drawn under my supervision from an actual survey made under my supervision recorded in deed book 1109, page 1341, and/or plat book 14, page 67, that the ratio of precision is 1':10,000, that this map was prepared in accordance with the General Statutes of North Carolina Chapter 89C.
my hand and seal on the 6, day of NOV, A.D. 20 07.

WILLIAM M. ALLEN, PLS



LAKE NORMAN

760 CONTOUR PER DEED BK.1015 PG. 1564 & VERIFIED IN FIELD

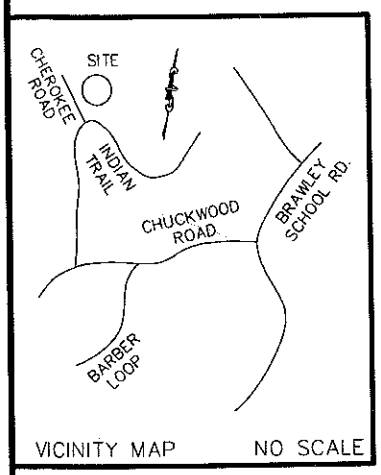

LOT 28
MICHAEL S. MANZ
798\520

LOT 27
0.60 AC.

LOT 26
THOMAS ARKLE III
1019\1600

PROPOSED HOUSE

50' SETBACK

35' FRONT SETBACK

15' SIDE SETBACK

15' SIDE SETBACK

N66°00'41"W 181.79 (BASE BEARING)

S 59°53'21" E 174.49'

S 32°50'10" W 134.56'

CONCRETE MONUMENT

TIE ONLY N05°42'50"E 139.20'

PK CL INTERSECTION

CHEROKEE ROAD (50' R\W)

R\W

R\W

E.I.P.

E.I.P.

E.I.P.

Drive

LINE TABLE		
LINE	LENGTH	BEARING
L1	20.15	N54°13'49"E
L2	16.61	N41°18'21"E
L3	18.48	N21°34'49"E
L4	8.84	N33°35'30"E
L5	17.55	N41°55'09"E
L6	21.77	N21°22'53"E
L7	13.86	N24°32'31"E
L8	16.16	N38°15'30"E
L9	24.46	N29°57'44"E
L10	9.83	S59°53'21"E
L11	7.65	N66°00'41"W

NOTES

1) THIS PROPERTY MAY BE SUBJECT TO ANY EASEMENTS AND/OR RIGHTS OF WAY OF RECORD.
2) ACREAGE COMPUTED BY THE COORDINATE METHOD.
3) UNDERGROUND POWER
4) NO GRID MONUMENT FOUND WITHIN 2000 FEET.
