DEPARTMENT OF ENVIRONMENT AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

Sheet ___ of ___
PROPERTY ID #: ___
COUNTY: ___

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

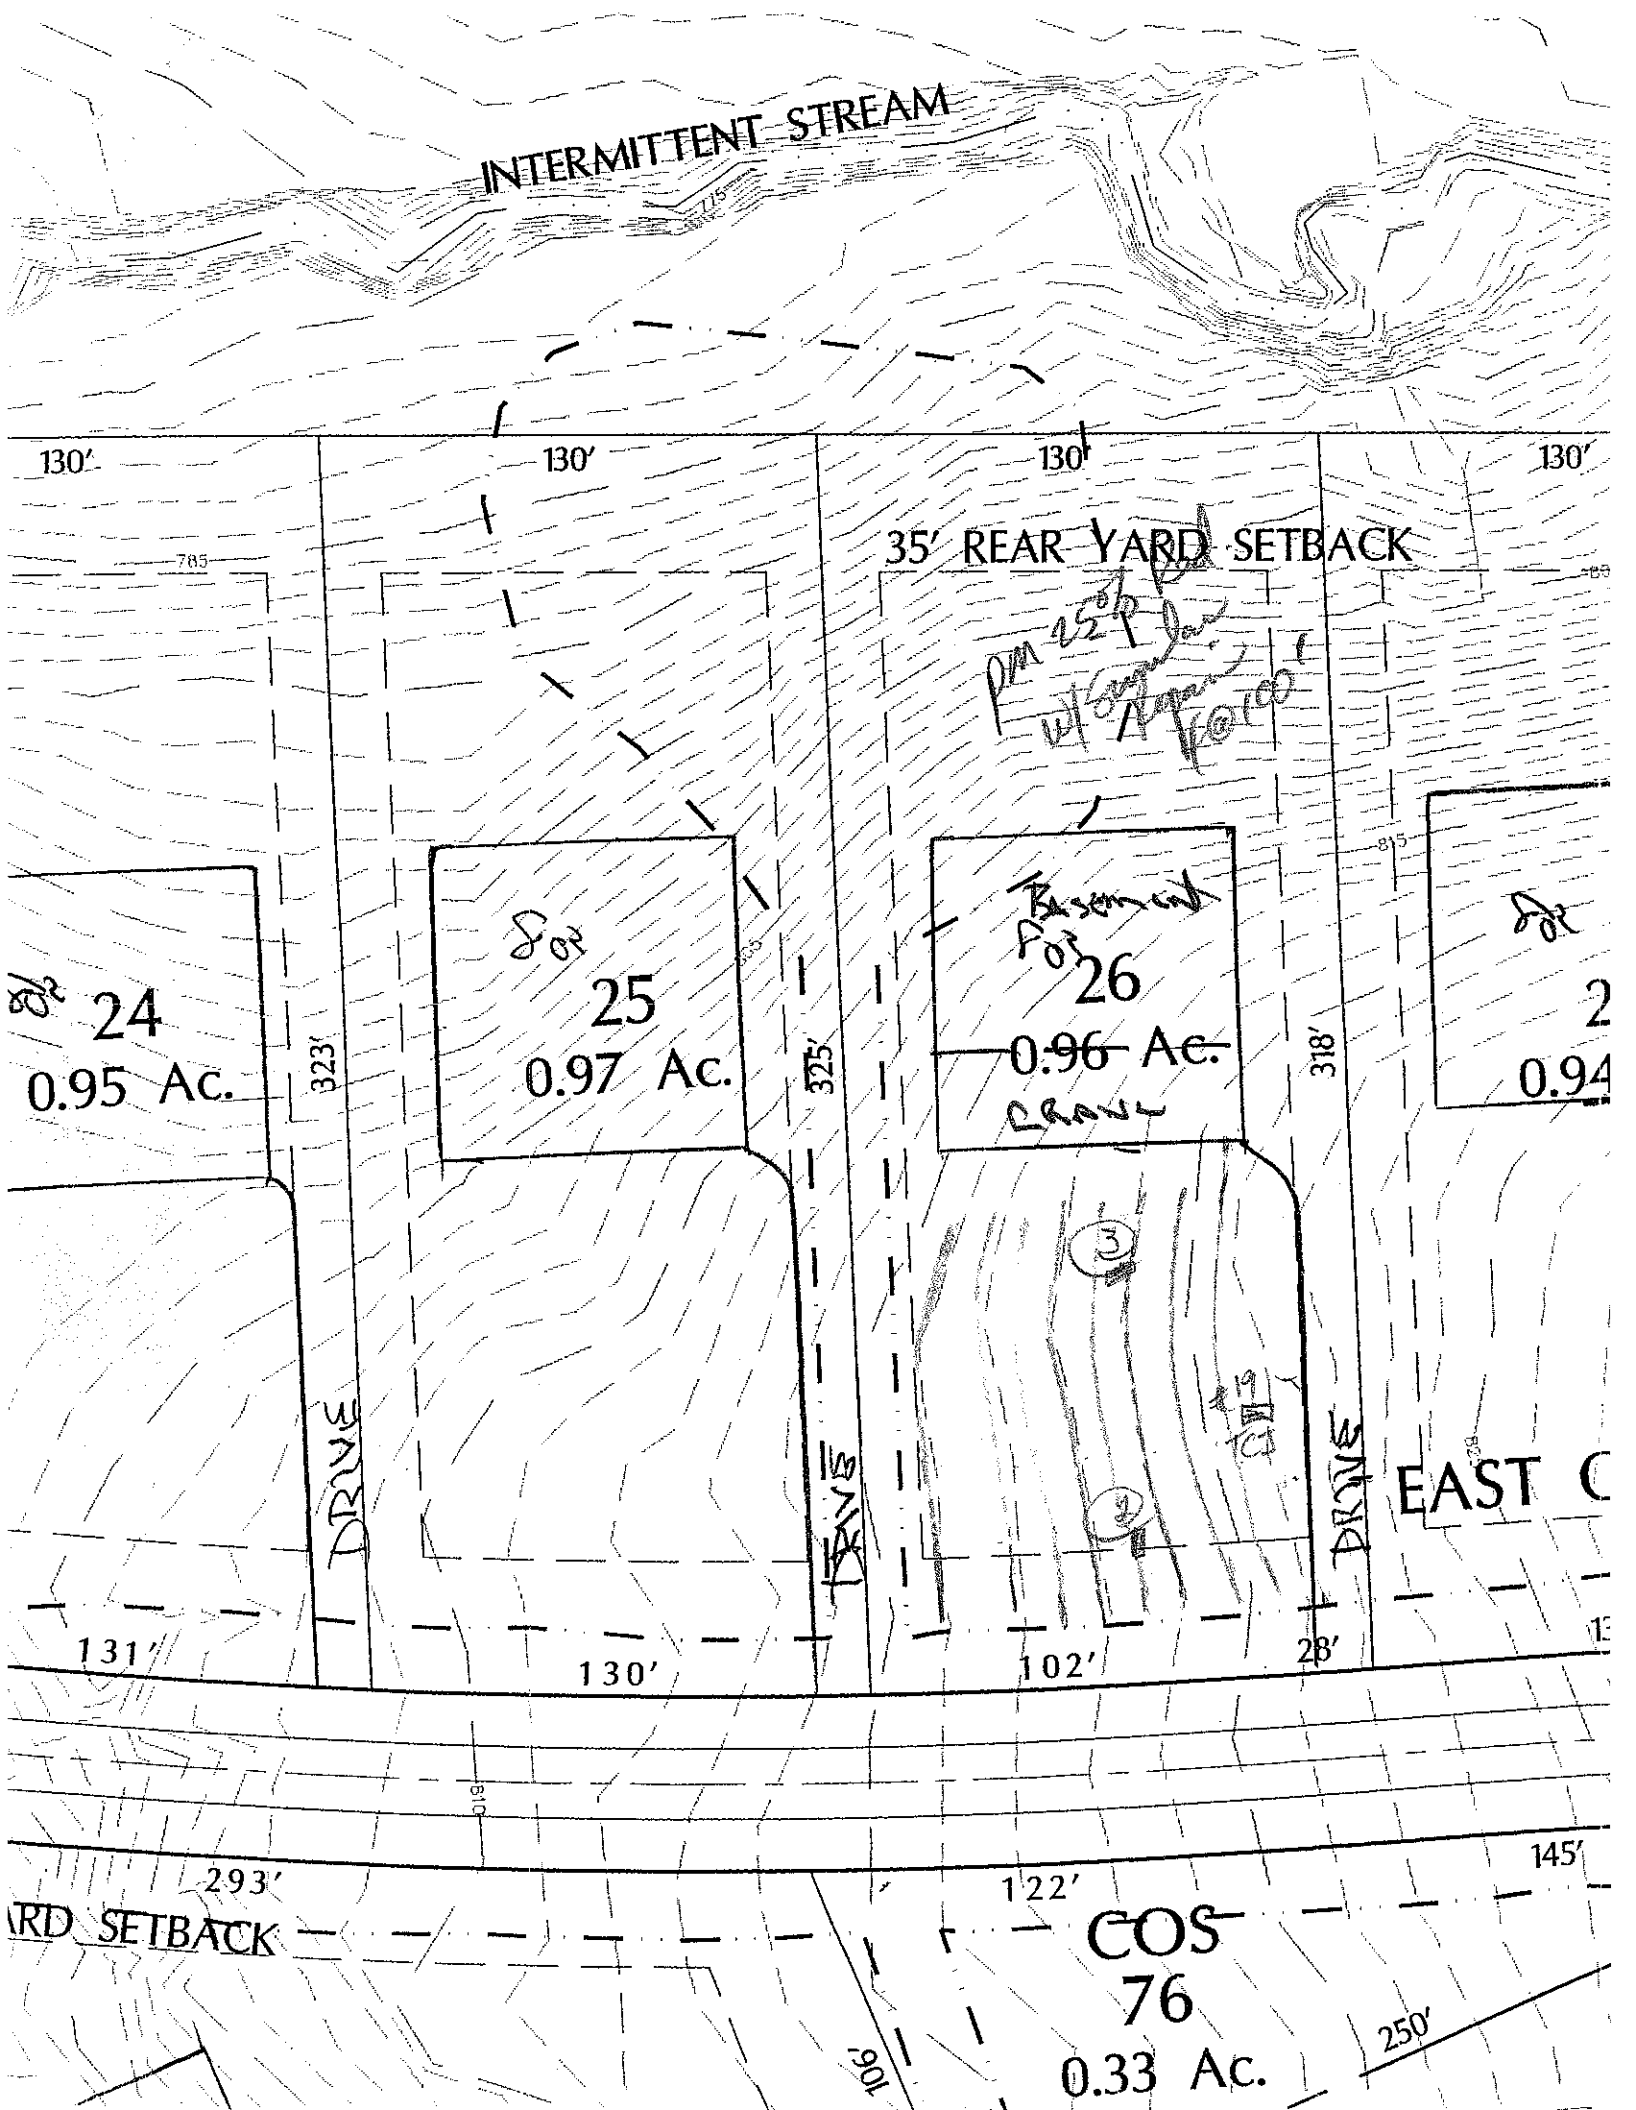
OWNER: ORI APPLICATION DATE ___
ADDRESS: ___ DATE EVALUATED: 3-26-03
PROPOSED FACILITY: ___ PROPOSED DESIGN FLOW (.1949): 480 gpd PROPERTY SIZE: ___
LOCATION OF SITE: lot 26 LAKE Forest PROPERTY RECORDED: ___
WATER SUPPLY: ☐ Private ☒ Public ☒ Well ☐ Spring ☐ Other ___
EVALUATION METHOD: ☐ Auger Boring ☒ Pit ☐ Cut
TYPE OF WASTEWATER: ☒ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	.1940 LAND-SCAPE POSITION/ SLOPE %	HORI-ZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	SOIL MORPHOLOGY (.1941) .1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	OTHER PROFILE FACTORS .1943 SOIL DEPTH	OTHER PROFILE FACTORS .1956 SAPRO CLASS	OTHER PROFILE FACTORS .1944 RESTR HORIZ	PROFILE CLASS & LTAR
1	#19 TC	0-5	gr sl bk R bansl	fr ss sp					
		5-45	m sbk RC cl	fr ss p	few fine mod sap				.3
2	6-8%	0-4	gr fsl	fr ss p					
		4-24	m-fsbk RC	fr ss p					
		24-50 (BC)	m-f sbk R cl	fr ss sp	common mod sap				.3
3		0-5	gr bansl	fr ss sp					
		5-31	m-f sbk RC	fi-fr ss sp	some				.3
		31-53 (BC)	m-f sbk yr cl	fr ss p	few mod sap				
4									

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	PS	PS
System Type(s)	PM 25% Red.	PM 25% Red. OR LPP/PDPS
Site LTAR	.3	.3

OTHER FACTORS (.1946): ___
SITE CLASSIFICATION (.1948): PS
EVALUATED BY: DJM
OTHER(S) PRESENT: Paul Pennington

COMMENTS: ___


INTERMITTENT STREAM
130'
130'
130'
130'
35' REAR YARD SETBACK
24
0.95 Ac.
323'
25
0.97 Ac.
325'
26
0.96 Ac.
318'
DRIVE
DRIVE
DRIVE
131'
130'
102'
28'
293'
122'
145'
COS
76
0.33 Ac.
250'
