Well properly abandoned 5/15/90 SCI

11141

IREDELL COUNTY HEALTH DEPARTMENT

(SEPTIC TANK) IMPROVEMENTS PERMIT AND CERTIFICATE OF COMPLETION

(Ground Absorption Sewage Disposal System -- G. S. Chapter 130-Article 13C)

OWNER OR CONTRACTOR Daniel J. Stageberg DATE April 11, 1990 PERMIT NO. 2L-A-21

PHONE: Business _____ Home _____

LOCATION 1100, TR Blume, TL Beaten Path ~ 1 mi on right

198 Beaten Path Rd. S. R. No. _____

SUBDIVISION NAME _____ LOT NO. 21 SECTION OR BLOCK NO. _____


House (✓) Mobile Home ( ) Business ( ) Other _____

No. Bedrooms	3	No. Bathrooms	3		
Garbage Disposal Unit	Yes (✓)	No ( )		Character & Porosity of Soil	clayey
Auto. Dishwasher	Yes (✓)	No ( )		Percolation Rate	.25 gpd/sq ft
Auto. Wash. Machine	Yes (✓)	No ( )		Topography	5% - 15% + 3'
Site Suitable	Yes ( )	No ( )		Depth to Water Table	
				Rock or other impervious formations	none obs.

Lot Area _____

_____ Basement with Plumbing _____ Basement without Plumbing _____ No Basement

* Existing well

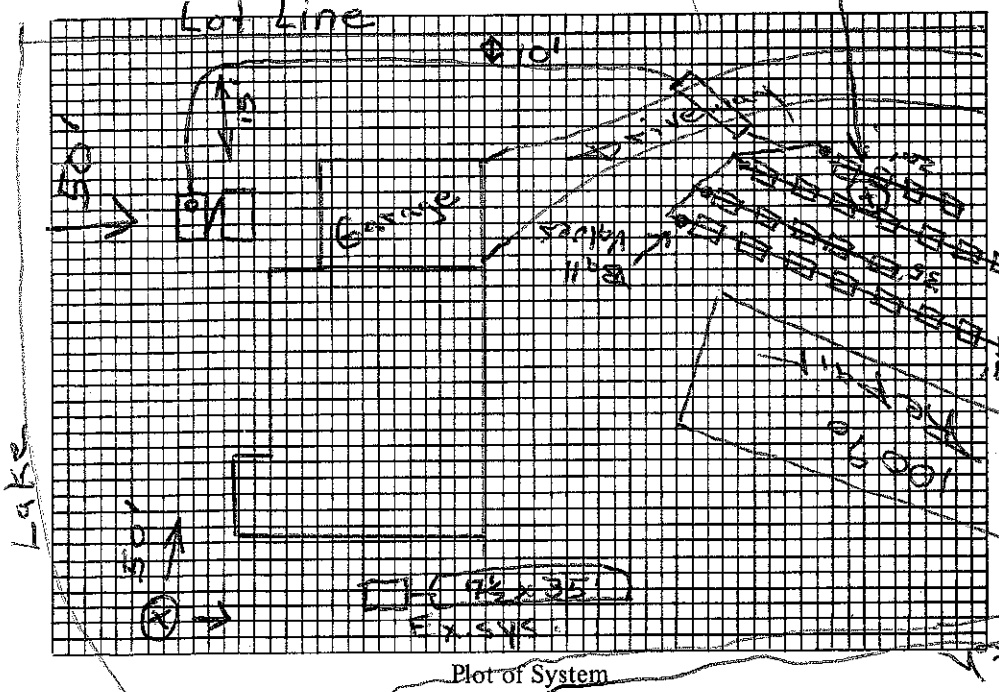

1250 Pump Tank

Size of Tank 1250 Gals.

Nitrification Field:

No. of Lines 4

Sq. Ft. _____ Linear Ft. 240'

Depth of Stone in Lines To T

Water Supply: Individual (✓) 16" Panel

Public ( ) 55 Panels

Installed by _____

I understand and agree to install septic tank system as specified on this Improvements Permit.

Signed Daniel J. Stageberg

IMPROVEMENTS PERMIT BY Sam Ingram EH-S

COMMENTS: (Supply Line) 2" 150' Schedule 40, (Laterals) 1¼" Sch. 40, 1 5/32" Hole per panel, Pump 23 gpm 27' TDH, * Existing Well Must Be Properly abandoned and verified by NRCD office

* Pipe underneath driveway must be sleeved in ductile iron

CERTIFICATE OF COMPLETION BY _____ DATE _____

EXISTING SYSTEM CHECKED BY: _____ DATE _____

CONSTRUCTION MUST COMPLY WITH ALL OTHER APPLICABLE STATE AND LOCAL REGULATIONS.

Permit is VOID if any unauthorized changes are made in installation of system and/or if any false information is supplied in making Improvements Permit.

Health Dept. Copy: White Inspection Dept. Copy: Yellow Sanitarian's Copy: Pink Owner's Copy: Gold

* Health Dept. will need to meet contractor on site before any alteration to drainfield area occurs.
