
Paul Calloway

Feb 17, 188

Proposal: To increase existing "Calloway" easement area approx 50' in width in order to accomodate sewage system repair.

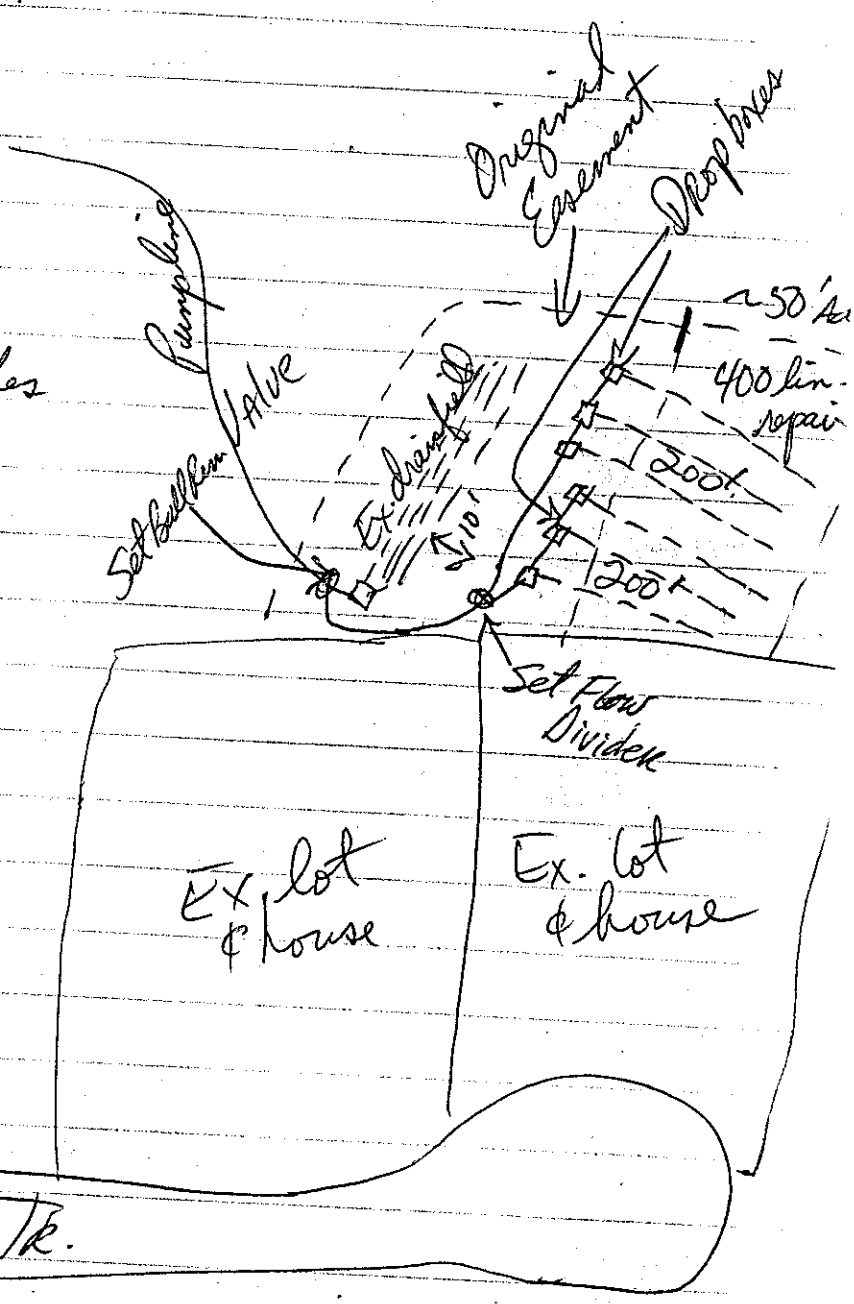

400 linear feet (1200 ft²) of repair line in 3' wide ditches 9' on center.

10,000–11,000 gal/month used based on meter results ~1.3–1.4 gal/ft²/day applrate

Old field to be shut off at least 1 year.

When additional easement is secured and recorded, and improvements permit will be issued.

David R. Hunter, RS
