
JUNE 24, 1993

SITE VISIT W/ BOB HARTIS (373-8428) OF CRESCENT RESOURCES TO CONDUCT SITE EVALUATION ON POSSIBLE EASEMENT AREA ACROSS ROAD.

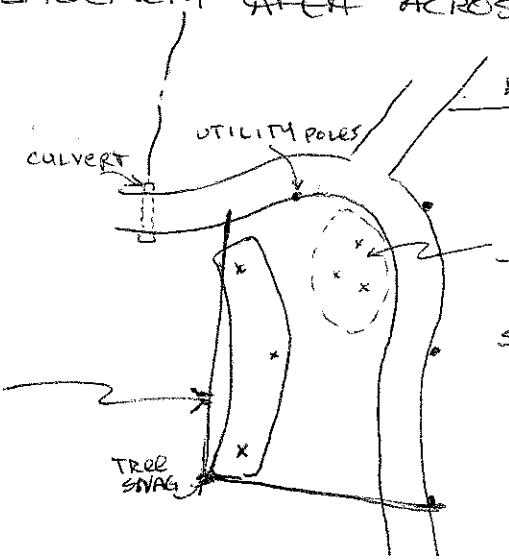

THIS AREA HAS SOILS CAPABLE OF SUPPORTING AN LPP SYSTEM

PROPOSED PROPERTY LINES TO ACHIEVE CONVENTIONAL SYSTEM W/ LPP REPAIR.

CLAY AND FINE SANDY CLAY FROM 0" TO 22" AND 24".

7/22/93

SITE VISIT W/ WESLEY SPARKS TO LAYOFF AREA NEEDED FOR NITRIFICATION FIELD. ADDITIONAL BORINGS MADE OVER LARGER AREA. FOUND SOIL CAPABLE OF SUPPORTING CONVENTIONAL SYSTEM & USE TOP OF HILL FOR LPP REPAIR.
