DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

PROPERTY ID #: _____
COUNTY: _____

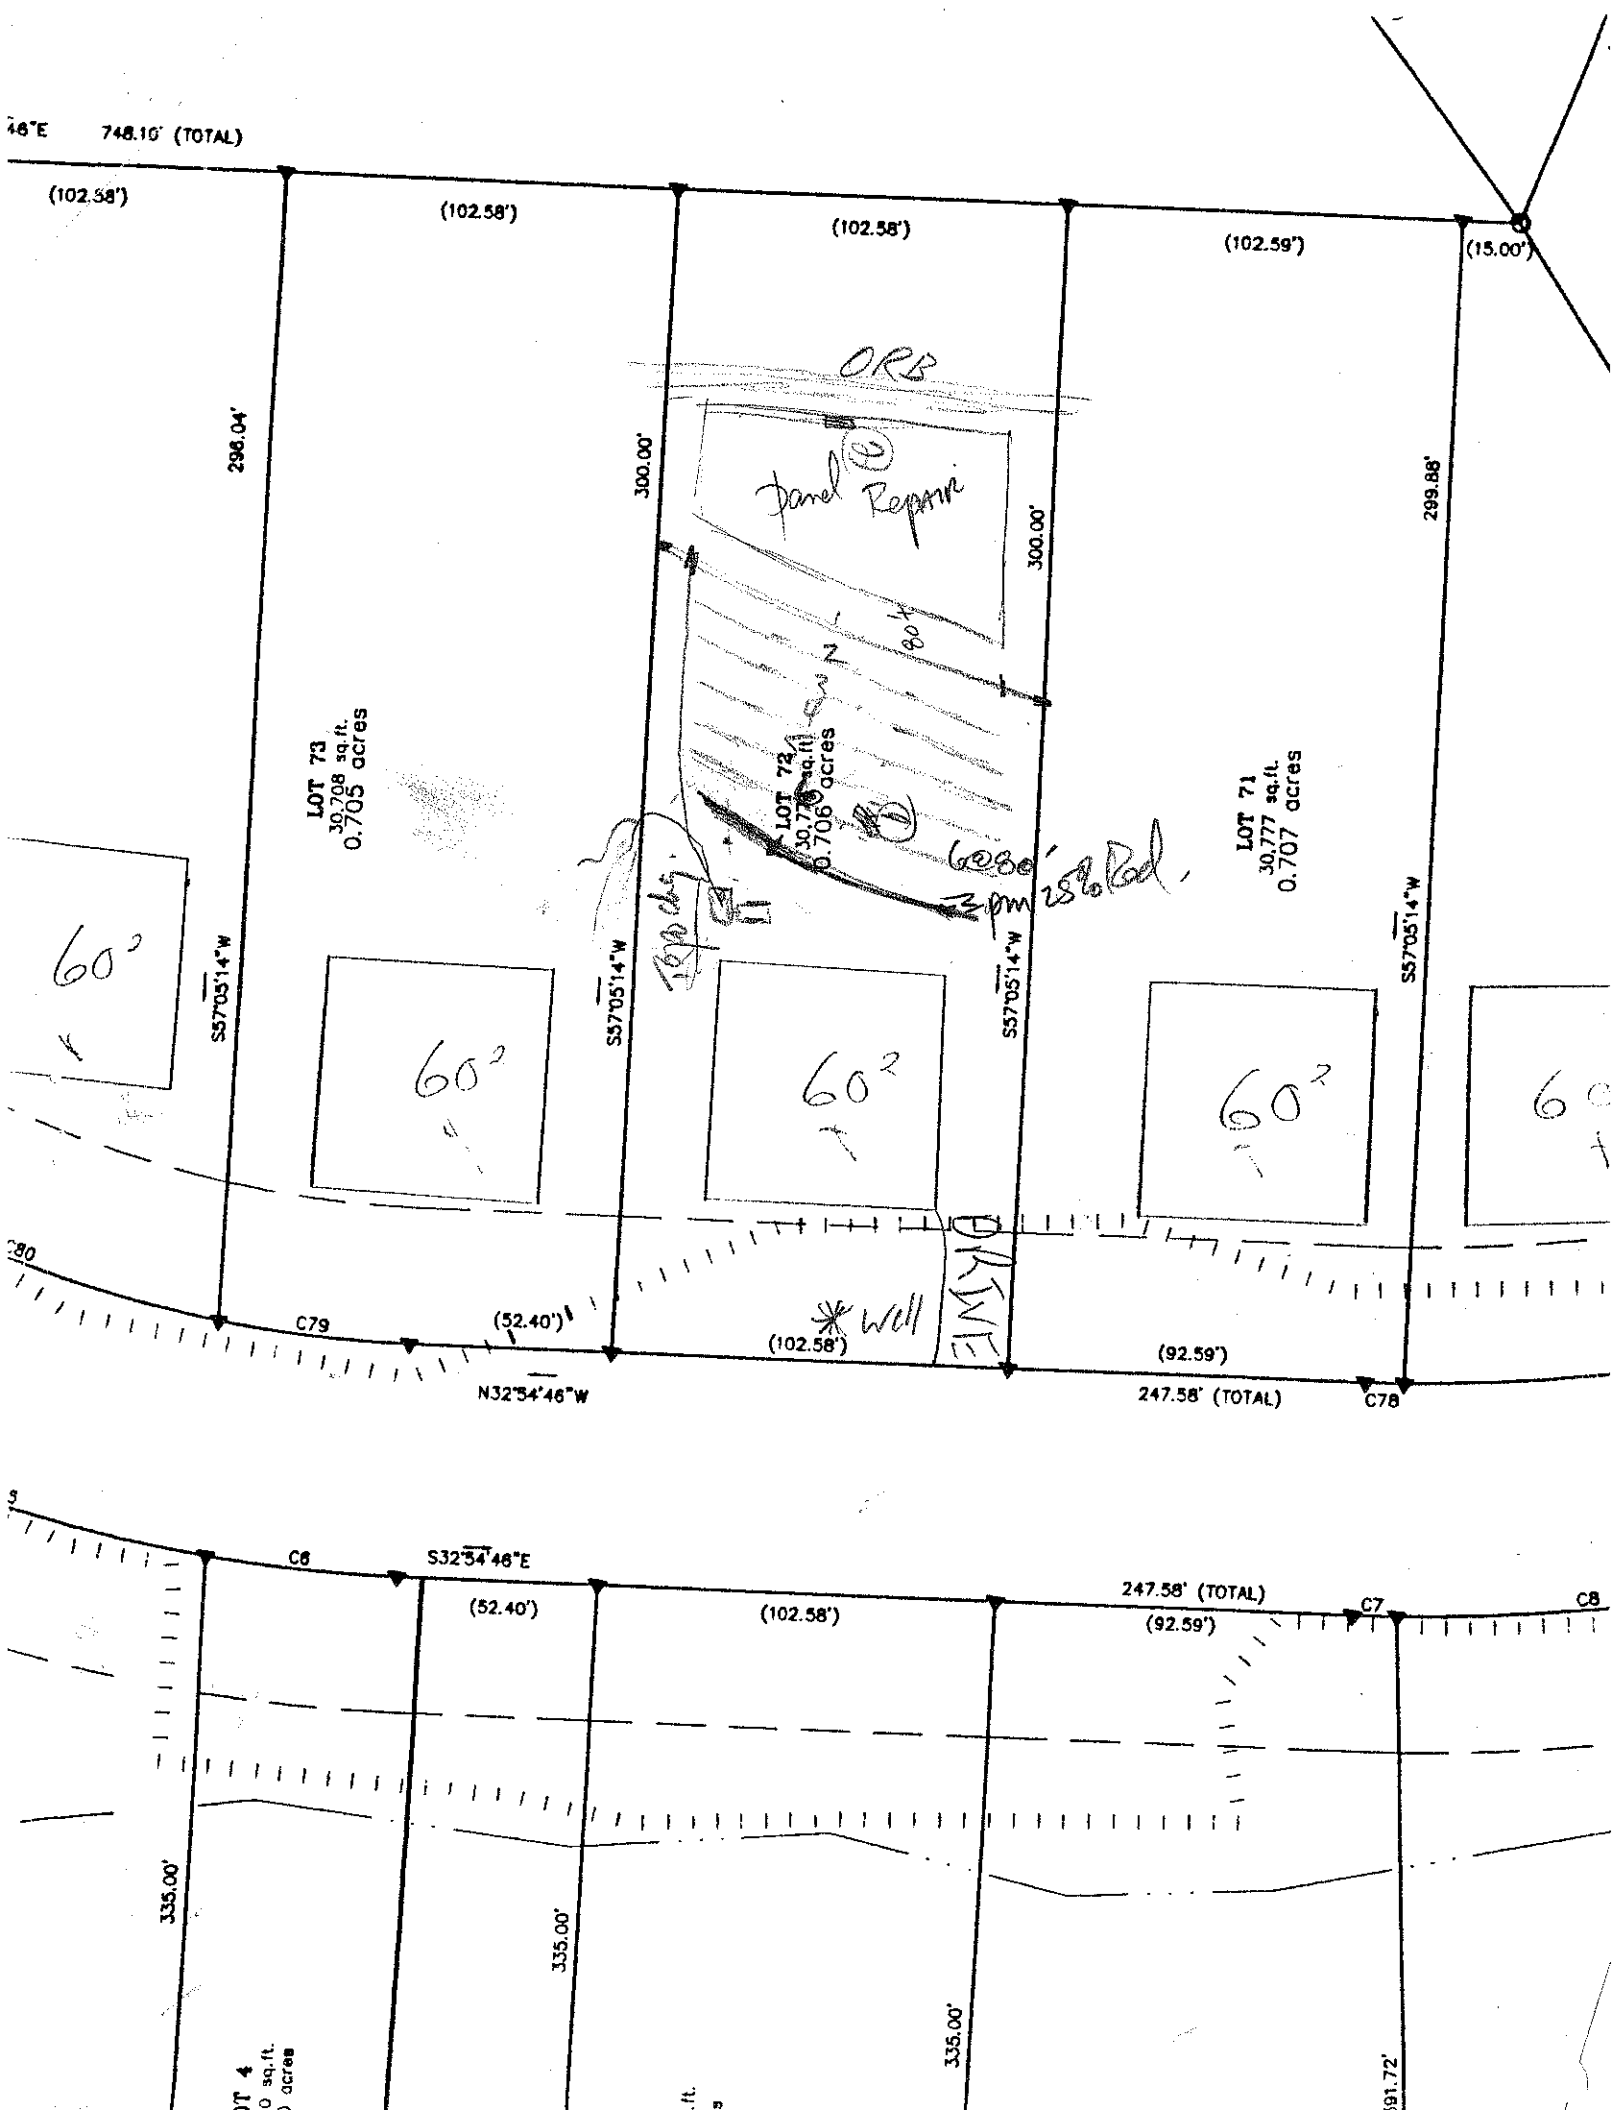
SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

OWNER: Shavender Dev Grp LLC APPLICANT: _____
ADDRESS: _____ APPLICATION DATE: _____ DATE EVALUATED: 10-15-04
PROPOSED FACILITY: SFR PROPOSED DESIGN FLOW (.1949): 4Bdrm pd PROPERTY SIZE: _____
LOCATION OF SITE: Lot 72 Northington Woods PROPERTY RECORDED: _____
WATER SUPPLY: ☒ Private ☐ Public ☒ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☐ Auger Boring ☒ Pit ☐ Cut
TYPE OF WASTEWATER: ☒ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	.1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	SOIL MORPHOLOGY (.1941) .1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LTAR
1	9%+ S/L	0-22	gr wk fsbk SL	fr SS SP					.3
		22-49	m fsbk RC	fr SP SS SP					
2		0-4	gr fsbk SL/SCL	fr					.25-.3
		4-32	m fsbk RC	fr SS SP	common yb/rd/gy mottles				
		32-52	wk fsbk Rcl	fr SS SP	common gy mottles				
3									
4									

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	PS	PS
System Type(s)	PM25% Rcd	LPPPBAS
Site LTAR	.25-.3	.25-.3

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): PS
EVALUATED BY: [signature]
OTHER(S) PRESENT: Paul Messenger


46"E 748.10' (TOTAL)
(102.58')
(102.58')
(102.58')
(102.59')
(15.00')
ORB
Panel Repair
298.04'
300.00'
300.00'
299.88'
LOT 73
30,708 sq.ft.
0.705 acres
LOT 72
30,776 sq.ft.
0.706 acres
LOT 71
30,777 sq.ft.
0.707 acres
60'
60'
60'
60'
S57°05'14"W
S57°05'14"W
S57°05'14"W
S57°05'14"W
C79
(52.40')
(102.58')
(92.59')
N32°54'46"W
247.58' (TOTAL)
C78
well
C6
S32°54'46"E
(52.40')
(102.58')
247.58' (TOTAL)
(92.59')
C7
C8
335.00'
335.00'
335.00'
