Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 1 OF 1
PIN #: 4648-32-0650
Lot #: 6
Permit #: 206443
AppID:

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

Owner: JOSEPH CUTRL
Applicant: SAME
Address: 245 NORTH AVE. SYRACUSE, NY
Date Evaluated: 12/12/2014
Proposed Facility: SFR Design Flow (.1949) 360
Property Size:
Location of Site: BEARSFOOT BAY LOT 6
Property Recorded: YES
Water Supply: [ ] Public [X] Individual [X] Well [ ] Spring [ ] Other
Evaluation Method: [X] Auger Boring [X] Pit [ ] Cut
Type of Wastewater: [X] Sewage [ ] Industrial Process [ ] Mixed

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	b PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
AB 1	SIDE 5%	0-48	FILL		NA	0"	NA	NA	U
AB 2	SIDE 6%	0-36	FILL		NA	12"	NA	48"+	U
		36-48	CL,M,SBK	SS					
PIT 1	SIDE 5%	0-48	FILL		NA	0"	NA	NA	U
PIT 2	SIDE 5%	0-42	FILL		NA	6"	NA	48"+	U
		42-48	RC,M,SBK						

Description	Initial System	Repair System
Available Space (.1945)	PS	PS
System Type(s)	PANEL BLOCK	PANEL BLOCK
Site LTAR	.3	.3

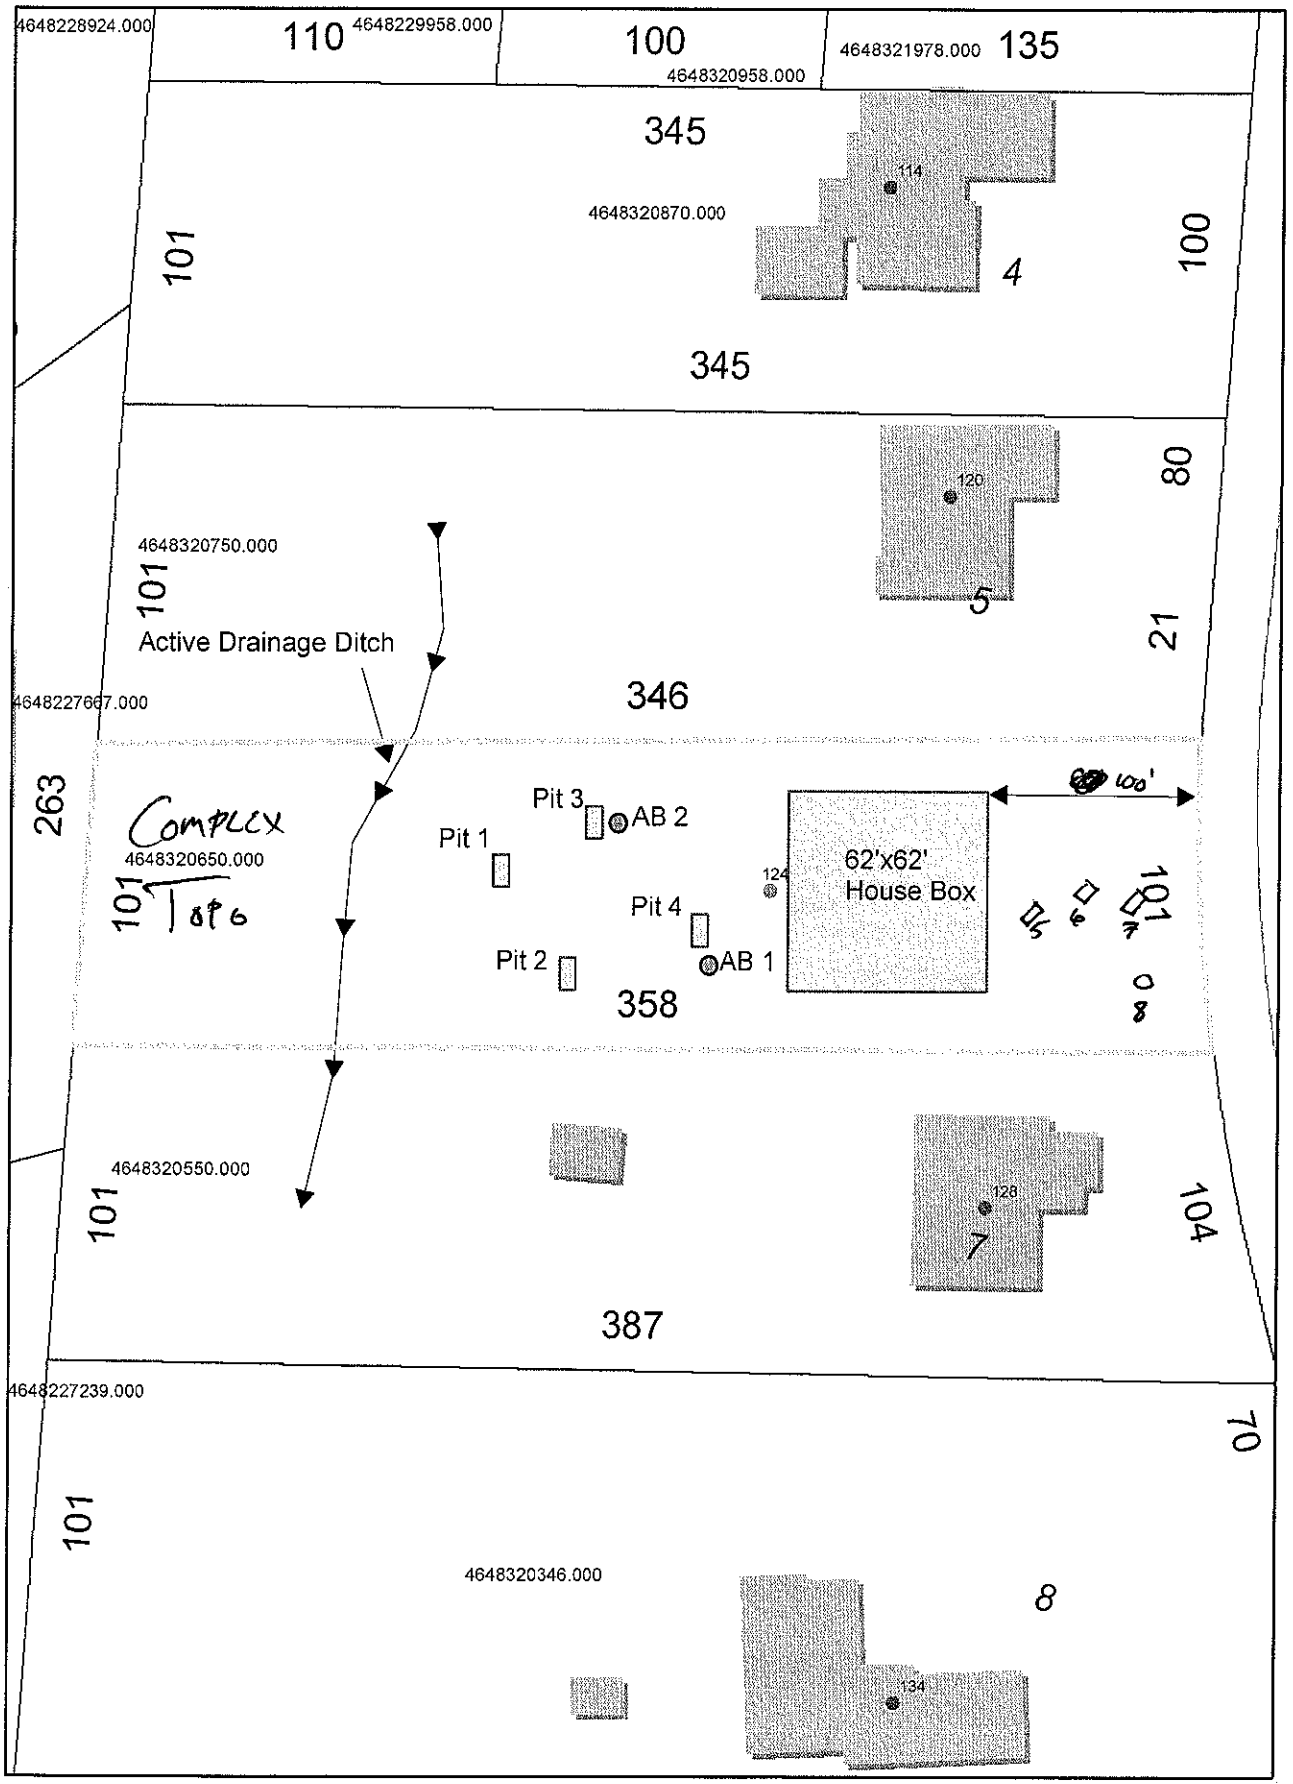
Other Factors (.1946):
Soil Evaluation By: BEN ALDRIDGE
Others Present: JAMIE O'DANIEL
Site Classification (.1948): PS
Site Evaluation By: BEN ALDRIDGE
Others Present: DUSTIN O'DANIEL

Department of Environment, Health, and Natural Resources
Division of Environmental Health
On-site Wastewater Section

Sheet: 2 OF 2
File #: 206443

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM
CONTINUED

PROFILE #	.1940 Landscape Position/ Slope%	Horizon Depth (IN.)	SOIL MORPHOLOGY .1941 .1941 Structure/ Texture	.1941 Consistence Mineralogy	OTHER PROFILE FACTORS .1942 Soil Wetness/ Color	.1943 Soil Depth (IN.)	.1956 Sapro Class	.1944 Restr Horiz	Profile Class & LTAR
PIT 3	SIDE 5%	0-43	FILL		NA	5"	NA	48"+	U
		43-48	RC,M,SBK	SS					
PIT 4	SIDE 5%	0-22	SCL,W,SBK	SS	NA	22"	S	48"+	.35
		22-60	LSAP	SS					
PIT 5	SIDE 5%	0-29	CL,M,SBK	SS	NA	48"	NA	48"+	.3
		29-48	C,M,SBK	SS					
PIT 6	SIDE 5%	0-26	SCL,W,SBK	SS	NA	48"	NA	48"+	.3
		26-48	C,M,SBK	SS					
PIT 7	SIDE 7%	0-48	C,M,SBK	SS	NA	48"	NA	48"+	0.3
AB 8	SIDE 5%	0-29	CL,M,SBK	SS	NA	48"	NA	48"+	0.3
		29-48	C,M,SBK	SS					


4648228924.000
110
4648229958.000
100
4648320958.000
4648321978.000
135
345
114
4648320870.000
101
4
100
345
120
80
4648320750.000
101
Active Drainage Ditch
5
21
4648227667.000
346
263
Complex
4648320650.000
101
Top 6
Pit 3
AB 2
Pit 1
124
62'x62'
House Box
100'
Pit 4
Pit 2
AB 1
358
101
4648320550.000
101
128
7
104
387
4648227239.000
70
101
4648320346.000
8
134
