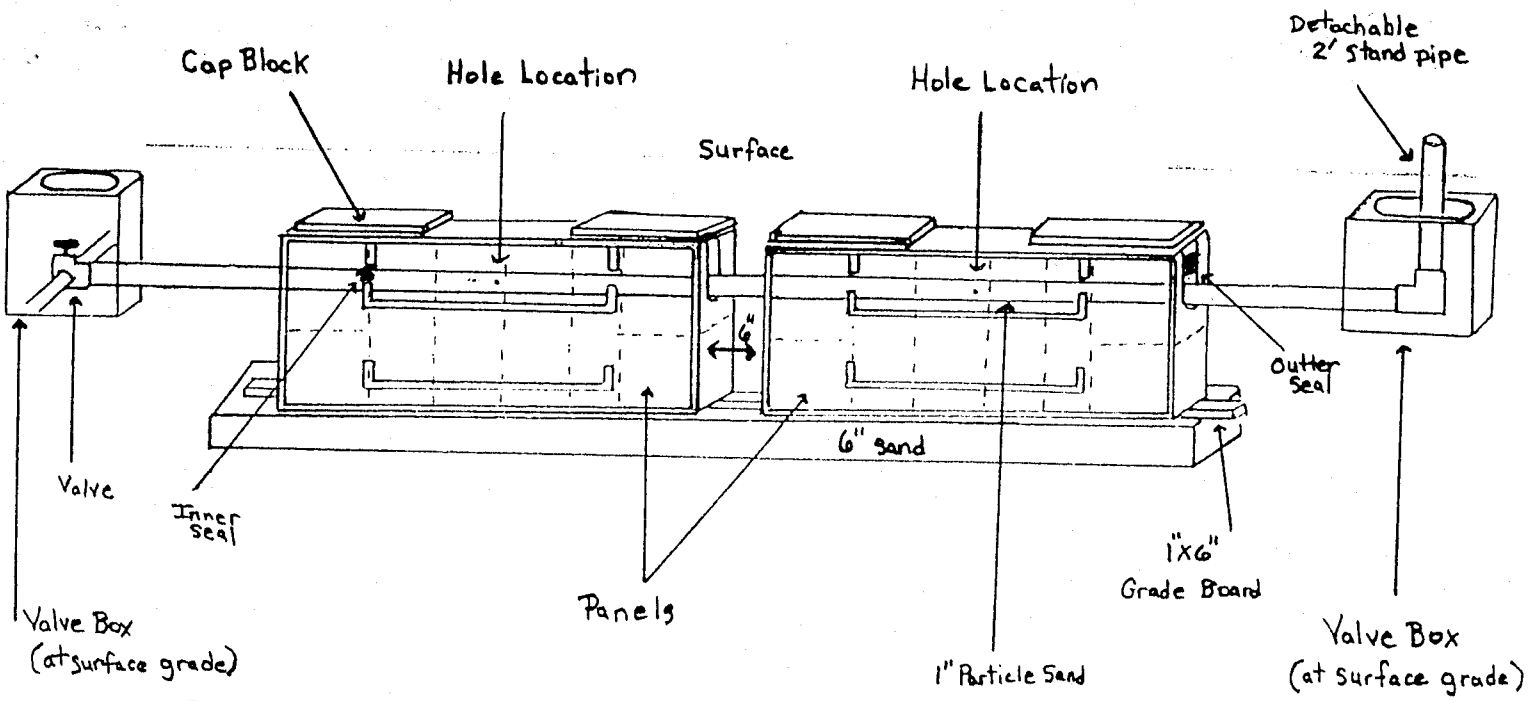


PD # 080956
HARBOR WATCH I LOT #2
PIN # 4710 49 1638
Pressure Dosed PPBPS

# of panels 60.
Size holes 3/16". 1 hole per panel.
Approximate amount of sand needed 45 TONS.
100 lbs. of partical sand per 8 panels.
Sidewalls raked and limed.
GPM 36.
TDH 51.

Comments

RAKE TRENCH SIDEWALLS AND APPLY LIME PRIOR TO INSTALLING PANELS
