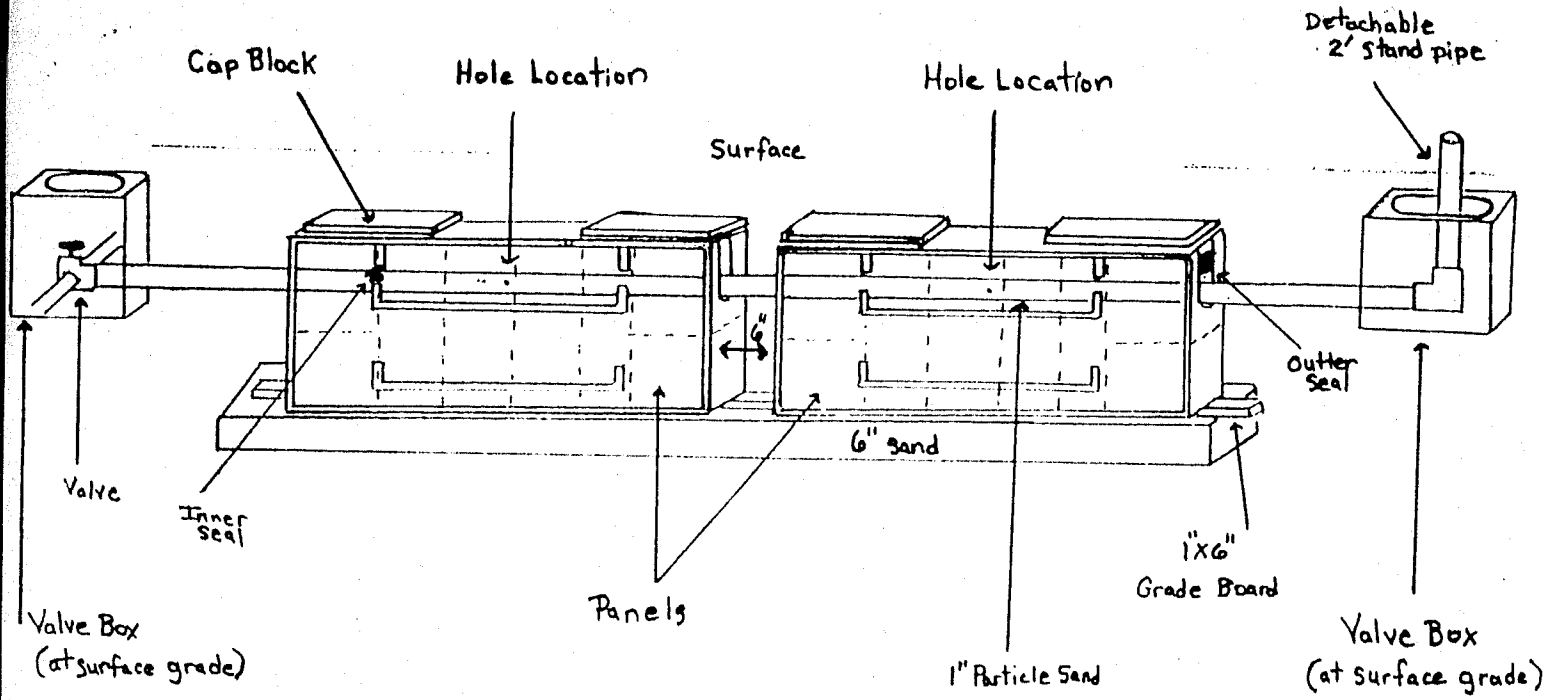



JEFFREY PLICHAT
#74566 WILDLIFE BAY II "53
Pressure Dosed PPBPS

# of panels 61.
Size holes 5/32". 1 hole per panel.
Approximate amount of sand needed 55.
100lbs. of partical sand per 8 panels.
Sidewalls raked and limed.
GPM 25.
TDH 50.

**Comments**

* RAKE TRENCH SIDEWALLS AND APPLY A LIGHT COATING OF LIME.
