
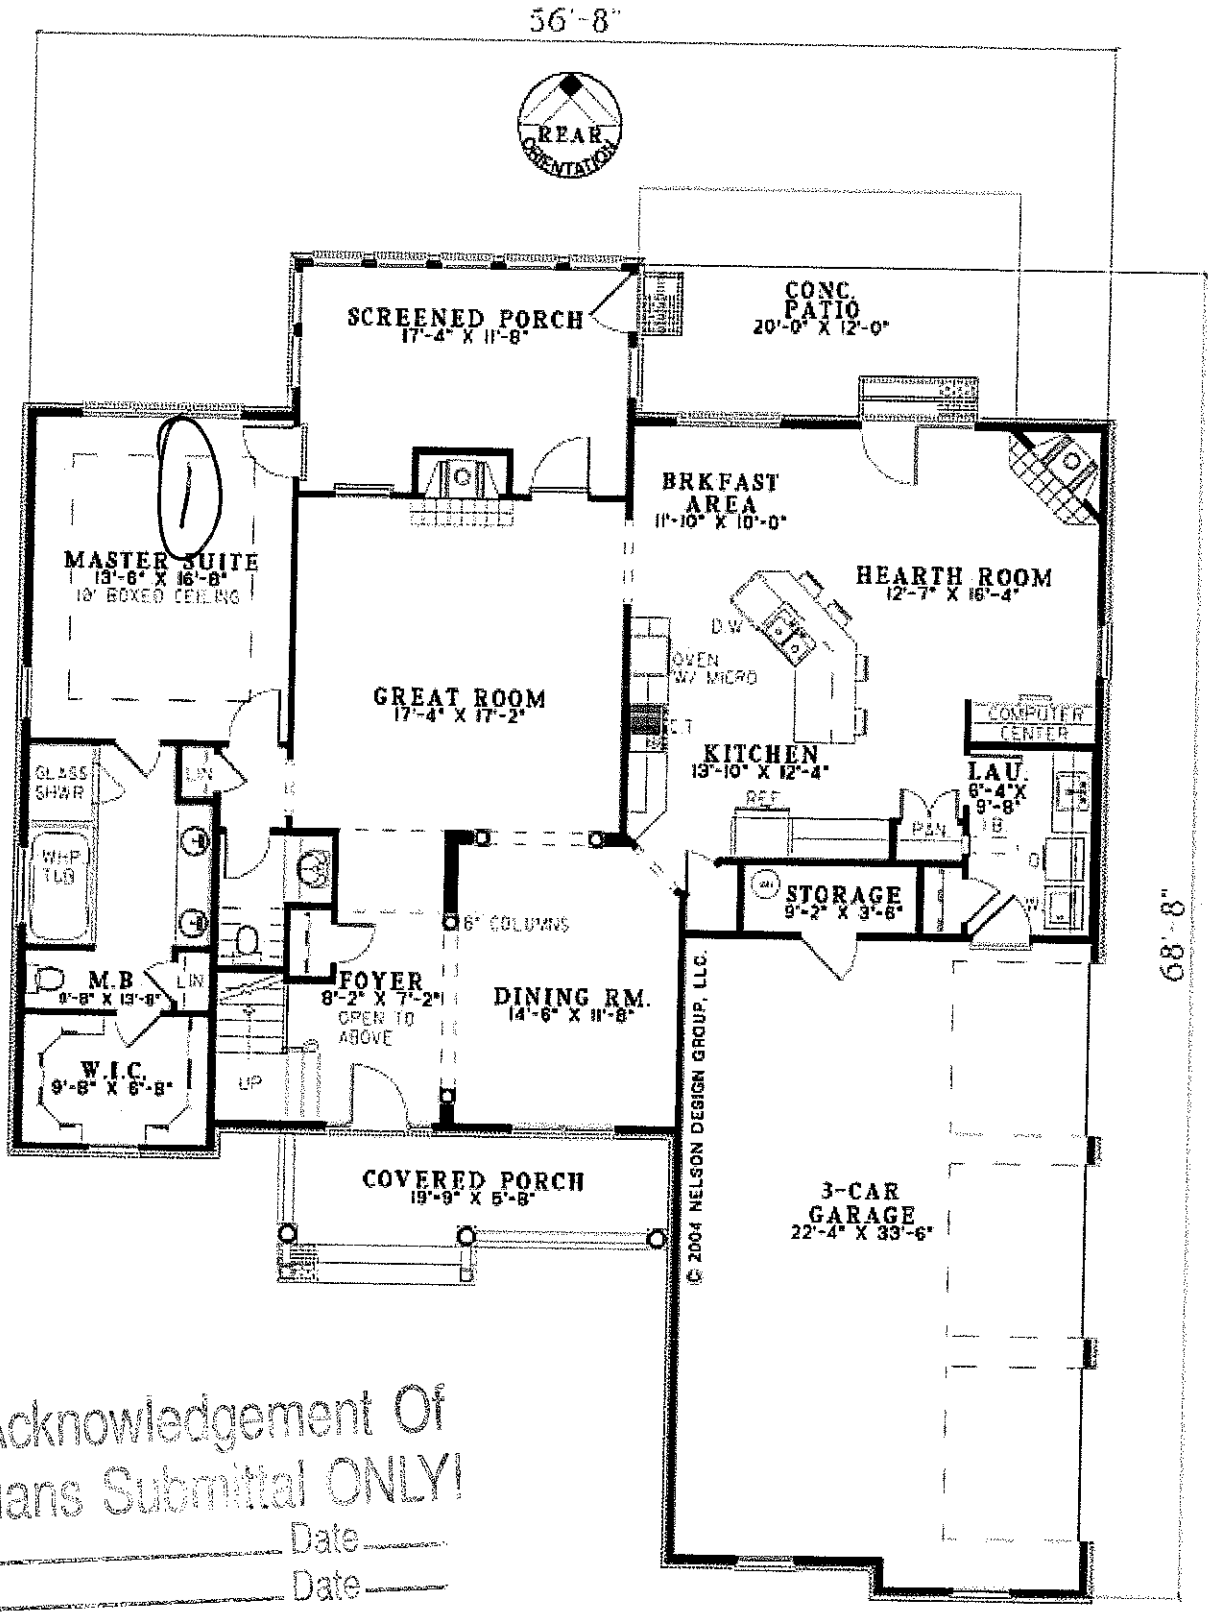


Acknowledgement Of
Plans Submittal ONLY!

_____ Date_____

_____ Date_____

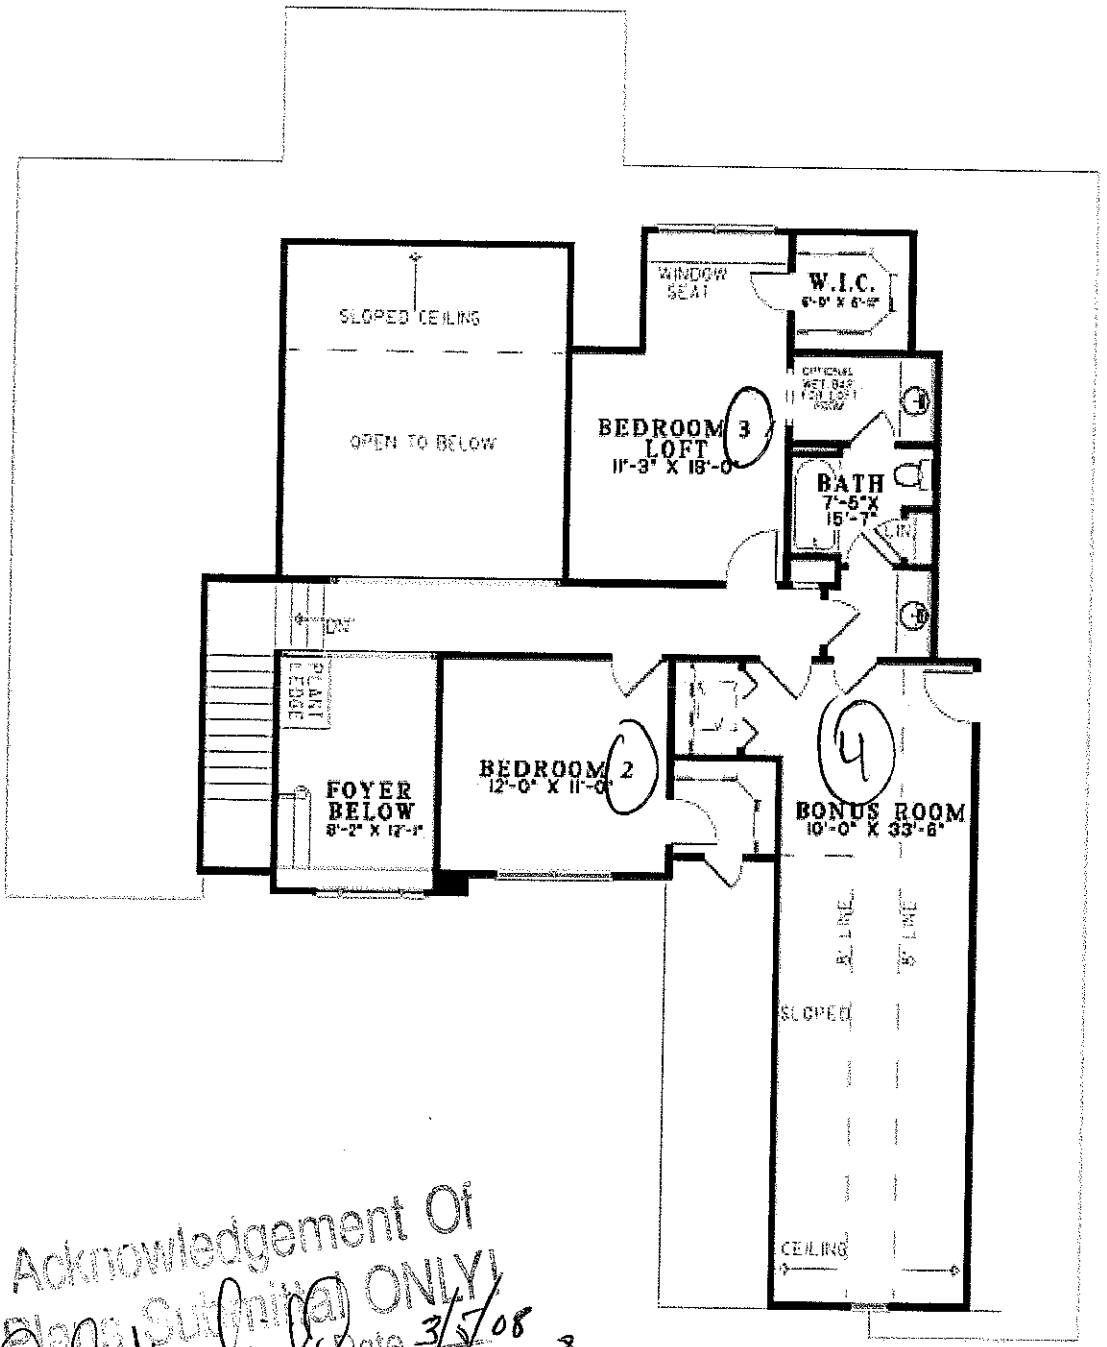

Acknowledgement Of Plans Submittal ONLY!

Date 3/5/08

Date 3-5-08

Buffalo Creek Dr. Lot 8

Project No. 5-1611

LAYOUT FOR A FOUR BEDROOM HOME

Nov-06

LINE #	FLAG COLOR	BS	HI	FS	ELEVATION	FLAGGED LINE LENGTH	Designed Length
TBM		6.2			100.0		
INSTR. 1			106.2				
			SYSTEM				
1	Blue			4.80	101.4	156	133
2	Pink			5.50	100.7	170	133
3	Yelow			6.60	99.6	187	133
						513	**399**
			REPAIR				
4	Yellow			7.50	98.7	210	200
5	Blue			8.50	97.7	220	200
					Total	**430**	**400**

	LINE LENGTH	LTAR GPD/FT^2	SYSTEM TYPE	INNOVATIVE TYPE	DISTRIBUTION
*** System**	399	0.30	Innovative	Chamber	Drop Box
Repair	400	0.30	Innovative	Chamber	Drop Box

Notes:

**TBM is assumed to be 100'

**All measures in feet

**Nitrification lines are demonstrated on contour via colored pin flags

**BS and FS indicate rod readings
