IREDELL COUNTY HEALTH DEPARTMENT

(SEPTIC TANK) IMPROVEMENTS PERMIT AND CERTIFICATE OF COMPLETION
(Ground Absorption Sewage Disposal System – G. S. Chapter 130-Article 13C)

OWNER OR CONTRACTOR Monticello Elem. School DATE 8 – 75 PERMIT NO. _____

PHONE: Business _____ Home _____

LOCATION _____

_____ S. R. No. _____

SUBDIVISION NAME _____ LOT NO. _____ SECTION OR BLOCK NO. _____

House ( ) Mobile Home ( ) Business ( ) Other School

No. Bedrooms _____ No. Bathrooms _____

Garbage Disposal Unit	Yes ( )	No ( )	
Auto. Dishwasher	Yes ( )	No ( )	
Auto. Wash. Machine	Yes ( )	No ( )	
Site Suitable	Yes ( )	No ( )	

Lot Area _____


Character & Porosity of Soil Red Clay

Percolation Rate 1" Per 60 minutes

Topography Level

Depth to Water Table Low

Rock or other impervious formations None

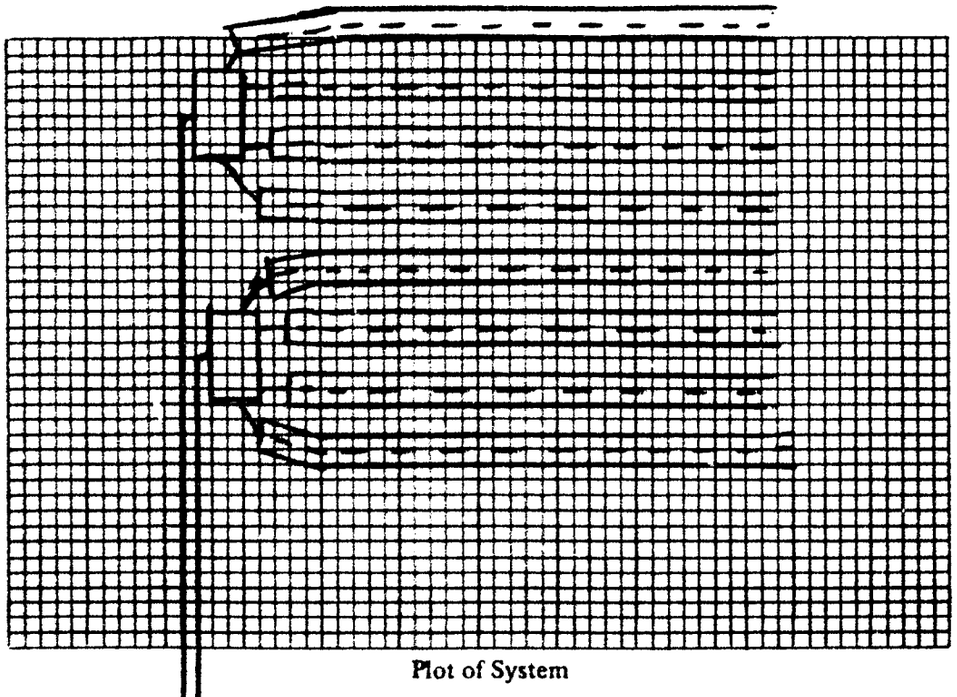

Plot of System

Size of Tank 3400 Gals.

Nitrification Field:
No. of Lines 8
Sq. Ft. 4500 Linear Ft. 1500
Depth of Stone in Lines 12"

Water Supply: Individual (✓)
Public ( )

Installed by Iredell County

IMPROVEMENTS PERMIT BY _____

COMMENTS: Trenches 188' Long 3' Wide 10' on Center. This system designed on information furnished by J.C. Murdock III Regional Engineer

CERTIFICATE OF COMPLETION BY E. A. Stevenson DATE _____

CONSTRUCTION MUST COMPLY WITH ALL OTHER APPLICABLE STATE AND LOCAL REGULATIONS.

Percolation Test Run by Iredell County Health Dept.

Health Dept. Copy: White Inspection Dept. Copy: Yellow Sanitarian's Copy: Pink Owner's Copy: Gold
