
James Hitt
ercrest
cH lot 152

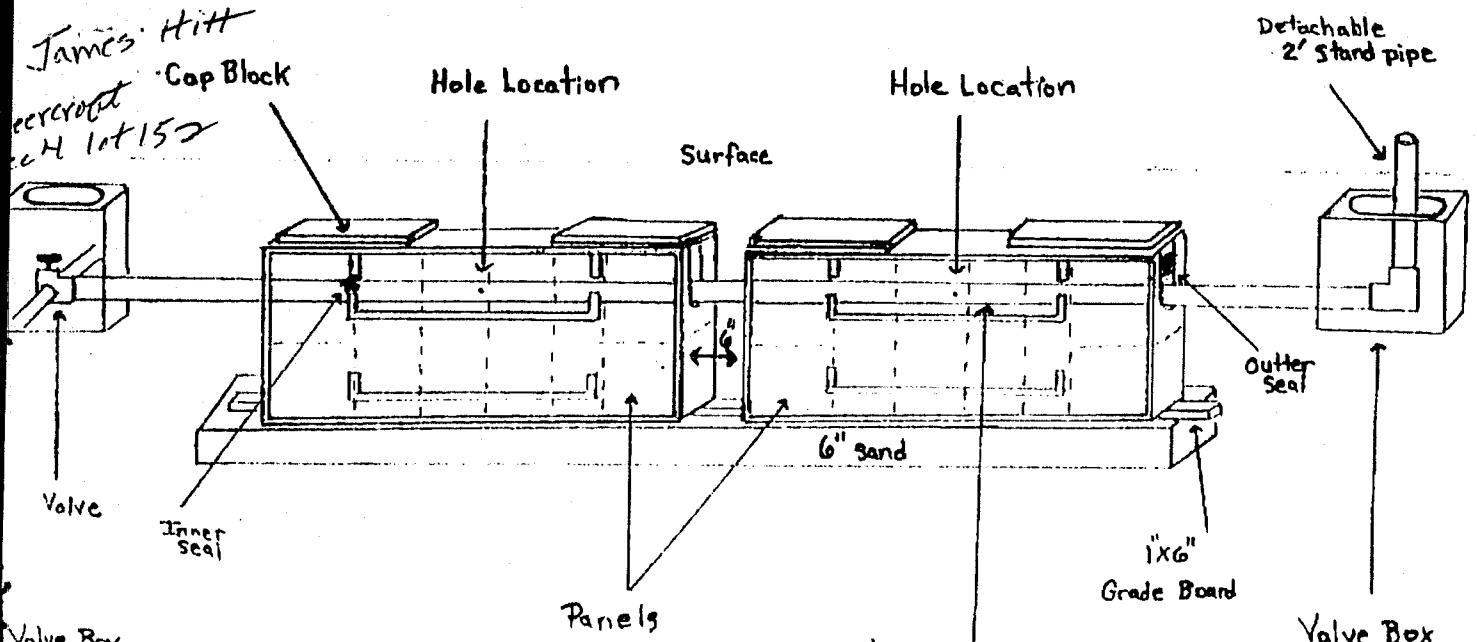

use centeral valve Box for all 4 valves as shown on Permit.

Pressure Dosed PPBPS

# of panels 64.
Size holes 3/16". 1 hole per panel.
Approximate amount of sand needed 50.
100lbs. of partical sand per 8 panels.
Sidewalls raked and limed.
GPM 40.
TDH 25.

Comments

08:25:96 TUE 09:40 FAX 704 464 5114 CCHD FIRST FLOOR 002
