
Norman Hope
Stonewall Lot 72

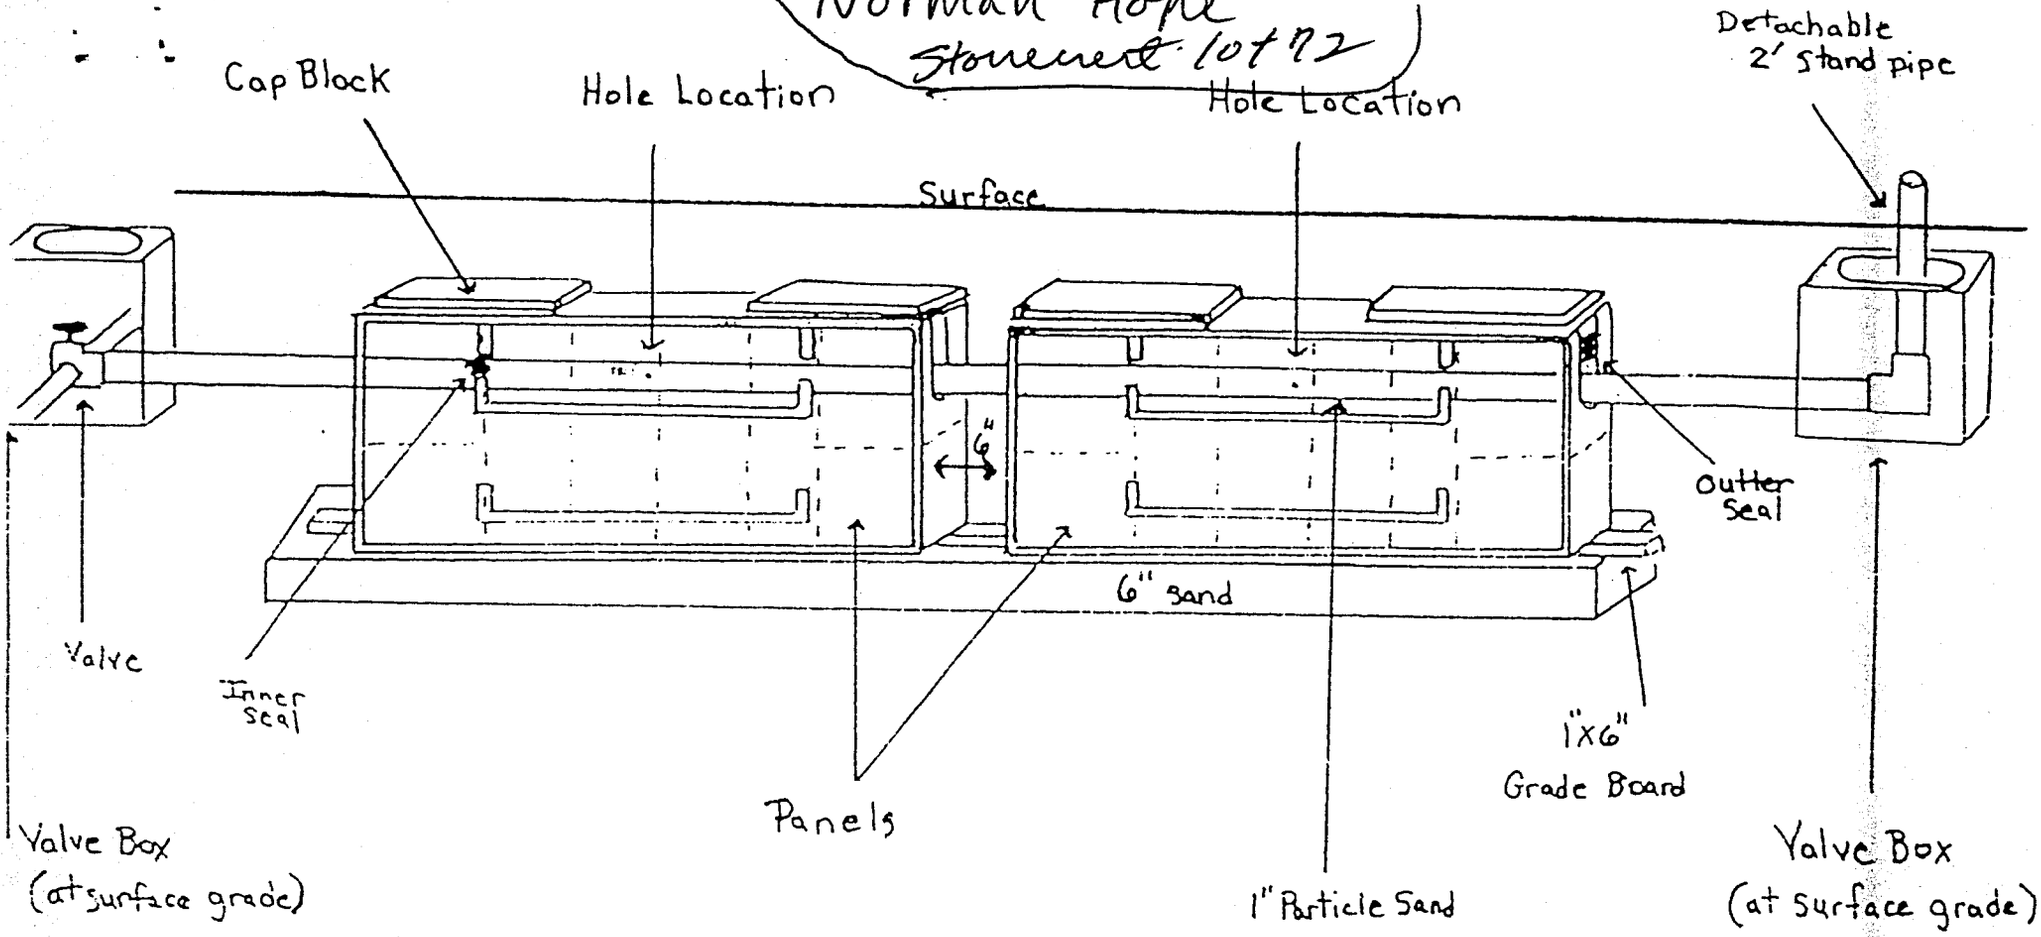

Pressure Dosed PPBPS

# of panels 46.
Size holes 3/16". 1 hole per panel.
Approximate amount of sand needed 33 Tons
100 lbs. of partical sand per 8 panels.
Sidewalls raked and limed.
GPM 30.
TDH 20.

Comments
