ICHD - ENVIRONMENTAL HEALTH DIVISION

Statesville Office (704) 878-5305 x3456 Mooresville Office (704) 660-3625

SEPTIC: IMPROVEMENT PERMIT / AUTHORIZATION TO CONSTRUCT / OPERATION PERMIT / EXISTING SYSTEM

PERMIT : OSWP 2024-47460

PIN # 4756 -- 05 -- 2074

APPLICANT/OWNER: Brad Tephabock APPLICANT ADDRESS: PO Box 100 Woodstock, Ga 30188

SITE ADDRESS: 127 Danbury Ln Statesville, NC 28625 PHONE: (302) 542-7215 ALT. PHONE -

SITE DIRECTIONS: Jane Sowers, Carl Austin SAP CONTROLLED: ☐ YES ☐ NO

SUBDIVISION: Danbury Forest SECTION: 52 LOT # 30 LOT AREA: - DESIGN FLOW: Ext L.T.A.R.(Initial): Ext L.T.A.R (Repair): Ext

Septic Tank 1000 (gal) STB Date

Pump Tank (gal) PT Date

Pump Make Model Serial #

Nitrification Fields Ext # Lines Ext Linear Ft Ext

Trench Width Ext *Max. Trench Depth(Initial) Ext *Max. Trench Depth(Repair) Ext Gravel Depth Ext

* Measured on the downhill side of the trench

☐ New System ☑ Repair ☐ Expansion System Type: I II (III) IV V VI

System Description: -

Repair System Description: Tank Replacement

Maintenance Agreement Required: ☐ YES ☑ NO

☑ GRAVITY ☐ PRESSURE

Effluent Standard: ☑ DSE ☐ HSE ☐ TS-I ☐ TS-II ☐ RCW ☐ NSF/ANSI 40

Usable Depth to LC (Initial): Ext

☑ Residence No. Bedrooms 3

☐ Business No. Persons 6

☐ Other No. Employees

☑ Slab ☐ Crawl Space

☐ Basement w/plumbing ☐ Basement w/o plumbing

Usable Depth to LC (Repair): Ext *Limiting Condition*

Water Supply


☐ Private

☑ Public

☐ Community

Comments / Conditions: Pump, Crush, fill new tank. Place new tank where proper fall can be achieved.

INITIAL SITE SKETCH

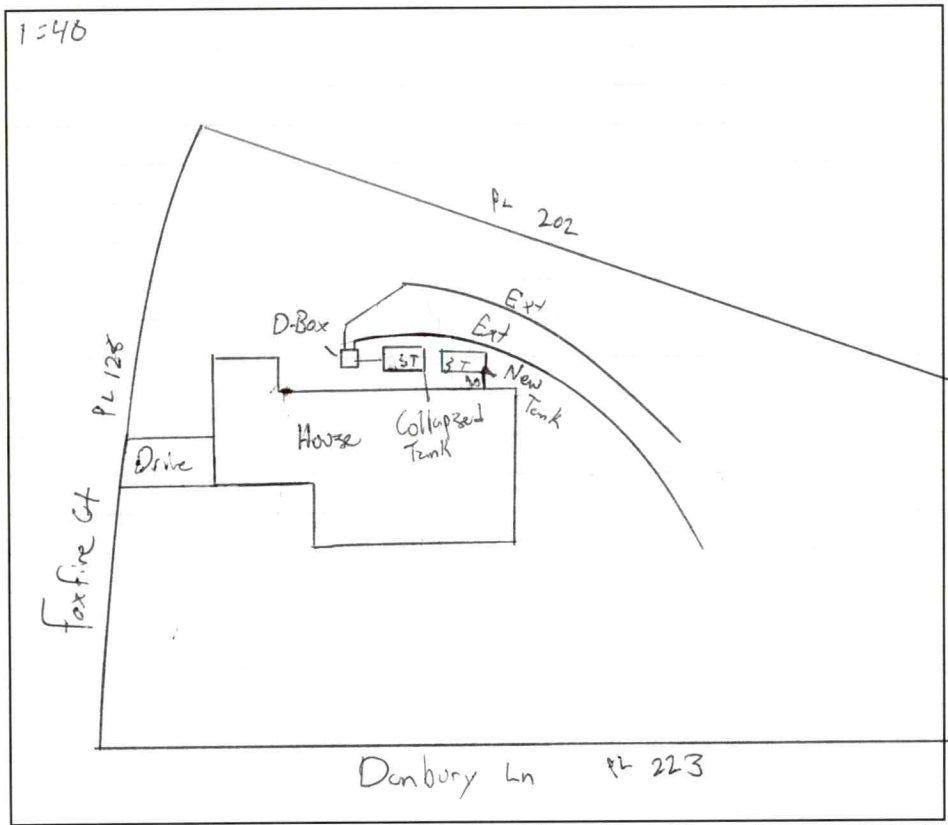

AS BUILT SKETCH

Installed as drawn

FOR SEPTIC FINAL INSPECTION CALL: 704-664-3703 between 8am-9am

the day the inspection is needed. Be sure to speak with an inspector to confirm your time.

Permit can be suspended or revoked if any false information is supplied toward securing the permit / any unauthorized changes are made to the site / any unauthorized changes are made in the installation of the system. **CONTACT A LOCATOR SERVICE PRIOR TO ANY EXCAVATION**

☐ **IMPROVEMENT PERMIT** ***with plat*** *valid without expiration.* ☑ **IMPROVEMENT PERMIT** ***with site plan*** *valid for 60 mos.* ☑ **AUTHORIZATION TO CONSTRUCT** *valid for period equal to IMPROVEMENT PERMIT--not to exceed 60 mo.*

Owner / Applicant Signature: Online Signature Date: Installed by: Kincaid Septic

IMPROVEMENT PERMIT by: Matt Wells Date: 2/27/24 OPERATION PERMIT by: Matt Wells Date: 4/16/24

AUTHORIZATION TO CONSTRUCT by: Matt Wells Date: 2/27/24 Existing System Inspected by: Date:

Item	Date	Initials
Drain Lines Checked		
Tanks Checked		
Pressure Manifold or Valve Box Checked		
Pressure Head Set		
Electrical Checked		
Floats Set		
Alarm Checked		
Maintenance Contract Needed? Y / N		
Comments:		

Repairs Only	
	State Code
Failing System Code	
Type of Distribution	G or P
Type of Failure/Malfunction	
Primary Cause of Failure/Malfunction	
Age of System? _____	
Initial or Repair? _____	

PERMIT SNAPSHOT REPORT OSWP-2024-47460 FOR IREDELL COUNTY

Permit Type	Environmental Health OSWP	**Project:**		**App Date:**	02/20/2024
Work Class:	EH Septic Permit	**District:**	Iredell County	**Exp Date:**	NOT AVAILABLE
Status:	PRIORITY PERMIT	**Square Feet:**	0.00	**Completed:**	NOT COMPLETED
Valuation:	$0.00	**Assigned To:**	Wilkinson, Matthew	**Approval Expire Date:**	
Description:	Repair tank				

Parcel: 4756052074.000 Main	**Address:** 127 Danbury Ln Statesville, NC 28625 Main	**Zone:** R-20(Suburban Residential District)

Property Owner	Applicant/Authorized Agent
Brad Tephabock	Brad Tephabock
Home: (302) 542-7215	PO Box 100
Mobile: (302) 542-7215	Woodstock, GA 30188
	Mobile: (302) 542-7215

Permit Custom Fields

How is your site plan being submitted	Custom Site Plan	Septic Application/Permit Type	Repair	Does the site contain any jurisdictional wetlands	No
Non-domestic Sewage Generated	No	Other Public Agency	No	All proposed structure dimensions	like kind, no changes in established location and measurements
Maximum Number of Bedrooms	3	If other Addition/Structure, please explain		Number of Occupants	0
Foundation Type	Concrete Slab Foundation	Residential/Business/Other	Residential	Water Supply	Municipal Water
Desired Septic System Type	Conventional (most common)	Additional Unique Setbacks Apply	No		


Attachment File Name	Added On	Added By	Attachment Group	Notes
Signature_Brad_Tephabock_2/20/2024.jpg	02/20/2024 15:08	Tephabock, Brad		Uploaded via CSS
Auth doc_v1.pdf	02/21/2024 7:46	Tephabock, Brad	Available Online	

Workflow Step / Action Name	Action Type	Start Date	End Date
Application Completeness Check v.1		02/21/2024 7:46	02/21/2024 7:47
Confirm application complete v.1	Generic Action		02/21/2024 7:47
~~**Zoning Review v.1**~~			02/21/2024 7:47
~~Floodplain Admin Overview v.1~~	Task		02/21/2024 7:47
~~Issue Invoice v.1~~	Generic Action		02/21/2024 7:47
~~Fees Paid v.1~~	Generic Action		02/21/2024 7:47
Fees v.1			
Issue Invoice v.1	Generic Action		
Fees Paid v.1	Generic Action		
Lot Readiness Verification v.1			
OSWP Septic Preliminary Site Visit v.1	Inspection		
OSWP Site Evaluation v.1	Inspection		
Issue Improvement Permit v.1			
Issue Invoice v.1	Generic Action		
Fees Paid v.1	Generic Action		
Issue Permit v.1	Generic Action		

PERMIT SNAPSHOT REPORT (OSWP-2024-47460)

Permit Completion Process v.1	
Authorization to Construct Permit v.1	Create Sub Permit
Issue Authorization to Construct v.1	Generic Action

Site Plan 127 Danbury Lane Statesville, NC

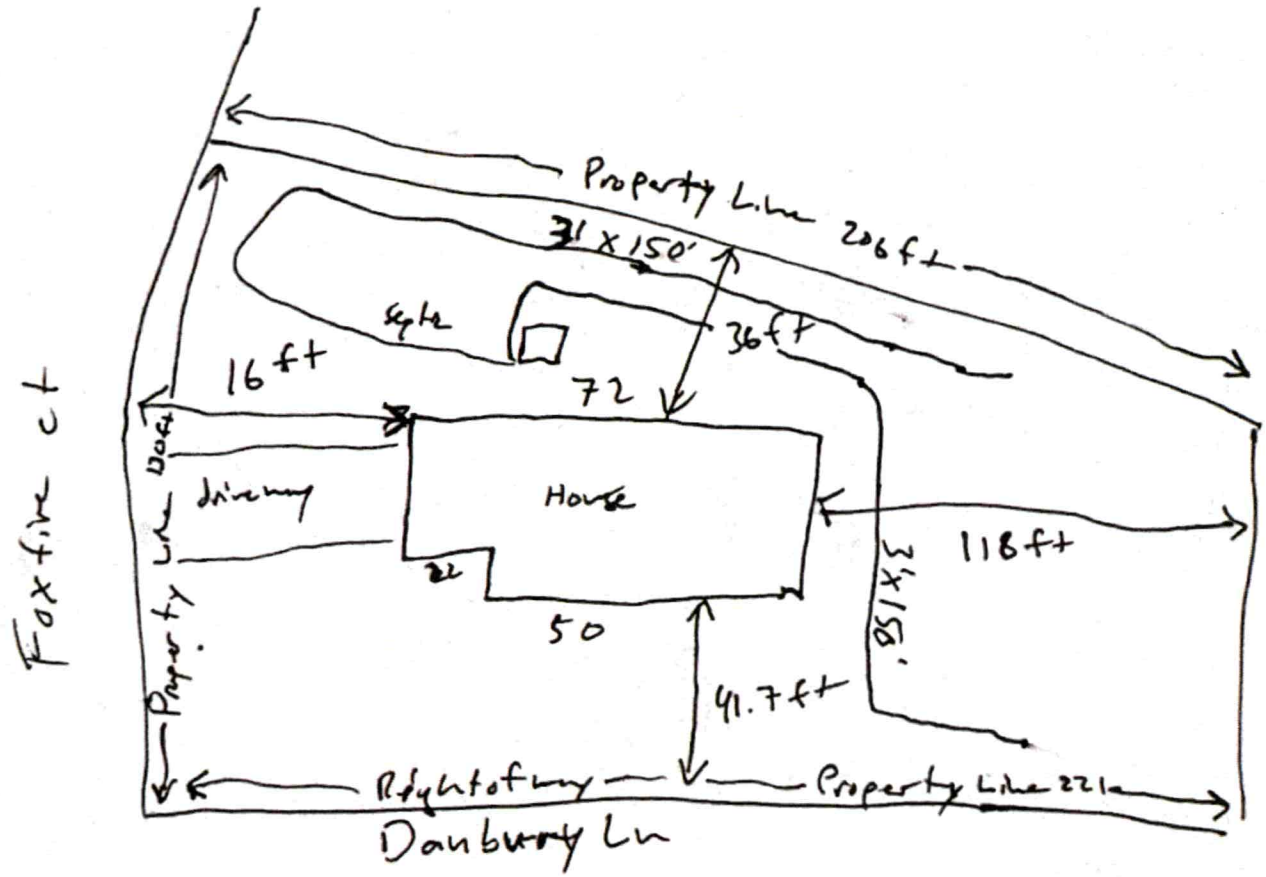

IREDELL COUNTY HEALTH DEPARTMENT

(SEPTIC TANK) IMPROVEMENTS PERMIT AND CERTIFICATE OF COMPLETION
(Ground Absorption Sewage Disposal System – G. S. Chapter 130-Article 13C)

OWNER OR CONTRACTOR Fortis Corp. DATE 4-25-80 PERMIT NO. _____

PHONE: Business _____ Home _____

LOCATION Rd 2171


S. R. No. _____

SUBDIVISION NAME Danbury Forest LOT NO. 30 SECTION OR BLOCK NO. _____

House (✓) Mobile Home ( ) Business ( ) Other _____

No. Bedrooms 3 No. Bathrooms 2
Garbage Disposal Unit Yes ( ) No (✓)
Auto. Dishwasher Yes (✓) No ( )
Auto. Wash. Machine Yes (✓) No ( )
Site Suitable Yes (✓) No ( )
Lot Area ½ acre

Character & Porosity of Soil Cecil Clay
Percolation Rate 120 min
Topography 2 to 4%
Depth to Water Table 10'+
Rock or other impervious formations none

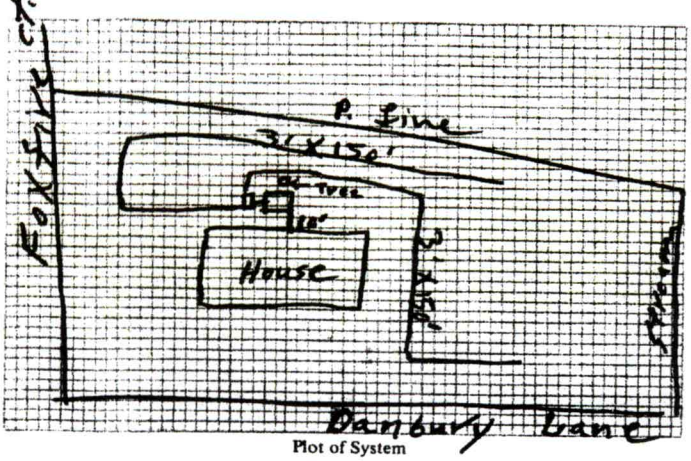

Plot of System

Size of Tank 1000 Gals.
Nitrification Field:
No. of Lines 2
Sq. Ft. 900 Linear Ft. 300
Depth of Stone in Lines 10"
Water Supply: Individual ( )
Public (✓)

Installed by Pfaff & Sale

IMPROVEMENTS PERMIT BY F. C. Moore

COMMENTS: Remove large Tree next to line. Also landscape & pipe Gutters so that surface water will not stand over lines or Tank.

CERTIFICATE OF COMPLETION BY F. C. Moore DATE 4-25-80

CONSTRUCTION MUST COMPLY WITH ALL OTHER APPLICABLE STATE AND LOCAL REGULATIONS.

Health Dept. Copy: White Inspection Dept. Copy: Yellow Sanitarian's Copy: Pink Owner's Copy: Gold


24
120
4756-05-1228
PB 1
72
4756-05-4209
4756-05-
114
4756-05-0177
112
193
91
110
4756-05-3104
4756-05-51
110
Foxfire Ct
29
127
128
4756-05-2074
4756-05-5034
30
223
241
Danbury Ln
PB 16-8
100
100
100
4756-04-0874
4756-04-1884
4756-04-2874
4756-04-3884
122
128
132
4756-04-48
