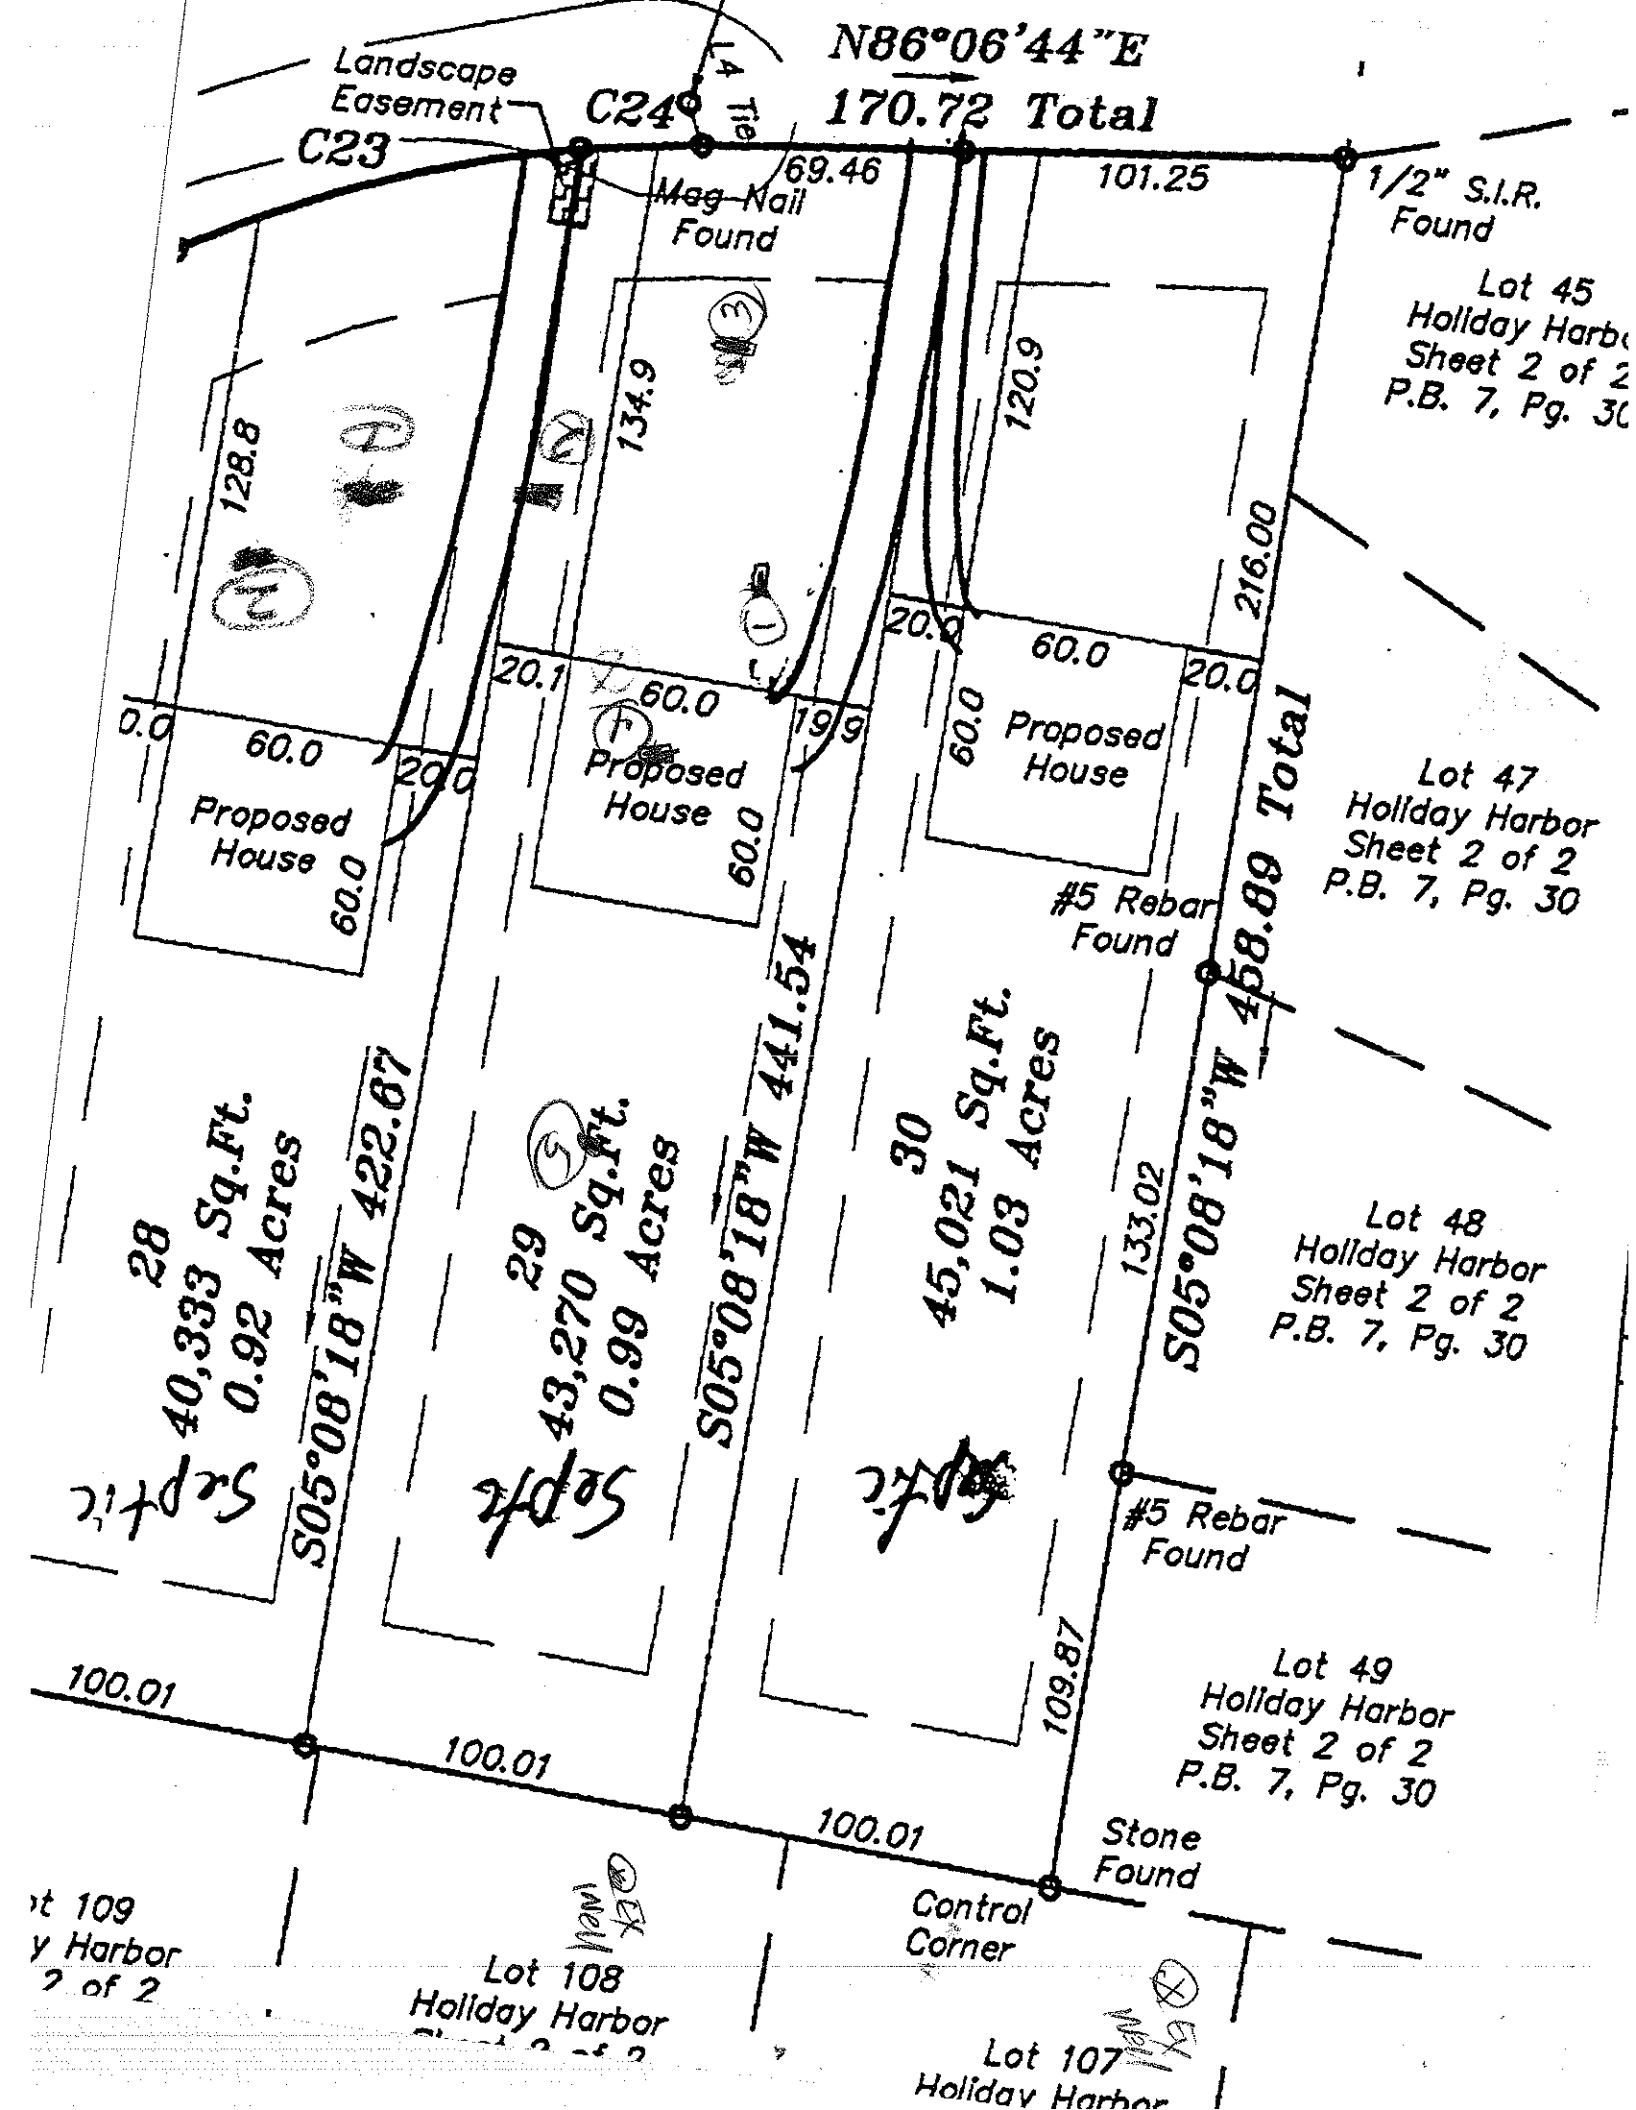

N86°06'44"E
170.72 Total
Landscape Easement
C24
C23
L4 Tie
69.46
Meg Nail Found
101.25
1/2" S.I.R. Found
Lot 45
Holliday Harbor
Sheet 2 of 2
P.B. 7, Pg. 30
128.8
134.9
120.9
216.00
0.0
60.0
20.0
20.1
60.0
19.9
20.0
60.0
20.0
Proposed House
Proposed House
Proposed House
60.0
60.0
60.0
#5 Rebar Found
Lot 47
Holliday Harbor
Sheet 2 of 2
P.B. 7, Pg. 30
28
40,333 Sq.Ft.
0.92 Acres
29
43,270 Sq.Ft.
0.99 Acres
30
45,021 Sq.Ft.
1.03 Acres
S05°08'18"W 422.67
S05°08'18"W 441.54
S05°08'18"W 458.89 Total
133.02
Lot 48
Holliday Harbor
Sheet 2 of 2
P.B. 7, Pg. 30
#5 Rebar Found
109.87
Lot 49
Holliday Harbor
Sheet 2 of 2
P.B. 7, Pg. 30
100.01
100.01
100.01
Stone Found
Control Corner
Lot 109
Holliday Harbor
Sheet 2 of 2
Lot 108
Holliday Harbor
Lot 107
Holliday Harbor

ENVIRONMENTAL HEALTH AND NATURAL RESOURCES
ON-SITE WASTEWATER SECTION

Sheet ___ of ___

SOIL/SITE EVALUATION for ON-SITE WASTEWATER SYSTEM

PROPERTY ID #:
COUNTY:

OWNER: Bill Bellune
ADDRESS:
APPLICANT:
PROPOSED FACILITY: SFR
APPLICATION DATE:
LOCATION OF SITE: Lot 29 Water Tree Landing
PROPOSED DESIGN FLOW (.1949): 480 gpd
DATE EVALUATED: 5-12-05
WATER SUPPLY: ☒ Private ☐ Public ☒ Well ☐ Spring ☐ Other
PROPERTY SIZE:
EVALUATION METHOD: ☐ Auger Boring ☒ Pit ☐ Cut
PROPERTY RECORDED:
TYPE OF WASTEWATER: ☒ Sewage ☐ Industrial Process ☐ Mixed

60' #5 0-5 SPR 1PC fr sssp SPRP 5-44+ wk sbk rcl fr ssp fri sp ●3 Repair Area

PROFILE #	.1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) STRUCTURE/ TEXTURE	SOIL MORPHOLOGY (.1941) CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LTAR
1	15% V	0-4	gr-wk sbk brn scl	fr					●3
		4-19	wk sbk RC	fr ss sp se p					
		19-28	wk sbk yr br cl	fr ss sp					
		28-60	wk sbk yr br cl	fr ss sp few common vf sap					
2		0-2	cr	fr ss sp					●3
		2-16	sbk RC	fr ss sp se p					
		16-44	wk sbk yr br cl	fr ss sp few sap					
		44-60	massive ss sap	fr ss sp					
3	5-26-05	0-7	wk sbk brn scl	fr ss sp					●3
		7-28	sbk RC	fr ss sp SPRP					
		28-62	wk sbk yr br cl	fr ss sp few vf sap					
		0-4	somewhat compacted scl	fi					●3 74"
		4-17	sbk RC	fr ss sp se p					
		17-54	wk sbk yr br cl	fr ss sp few common vf sap					

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
ilable Space (.1945)	PS	PS
em Type(s)	Conv 25% Red	Bed w/ pumped 25% Red
LTAR	●3	●3

OTHER FACTORS (.1946):
SITE CLASSIFICATION (.1948): PS
EVALUATED BY:
OTHER(S) PRESENT: Bill Bellune
