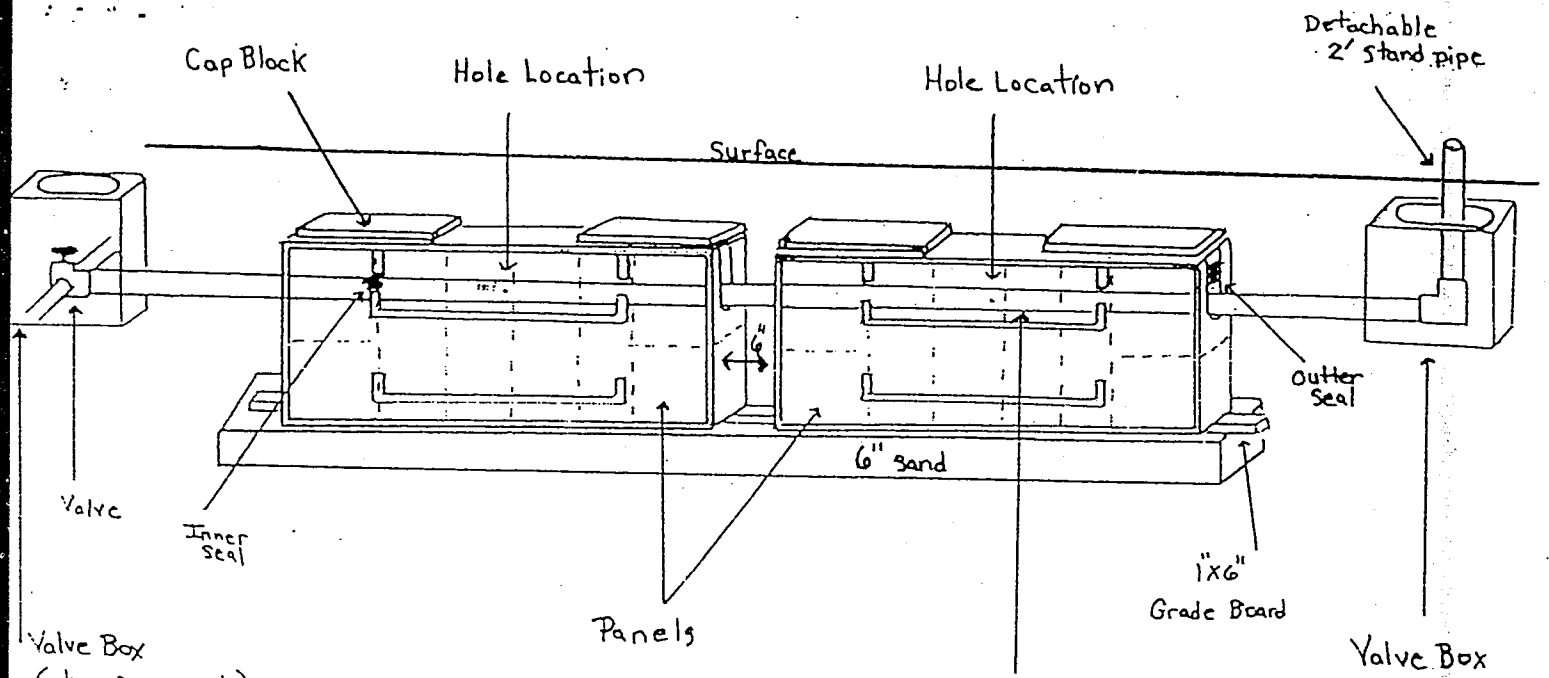


PP NO. 24846 Tax map 3C-2-A-75 Pkg

Section 17 Lot 880

Pressure Dosed PPBPS

# of panels 46.
Size holes 3/16". 1 hole per panel.
Approximate amount of sand needed 33 Tons.
100 lbs. of partical sand per 8 panels.
Sidewalls raked and limed.
GPM 30.
TDH 50.

Comments

S E I E 0 0
