DEPARTMENT OF ENVIRONMENT, HEALTH, AND NATURAL RESOURCES
DIVISION OF ENVIRONMENTAL HEALTH
ON-SITE WASTEWATER SECTION

Sheet ___ of ___
PROPERTY ID #: _____
COUNTY: _____

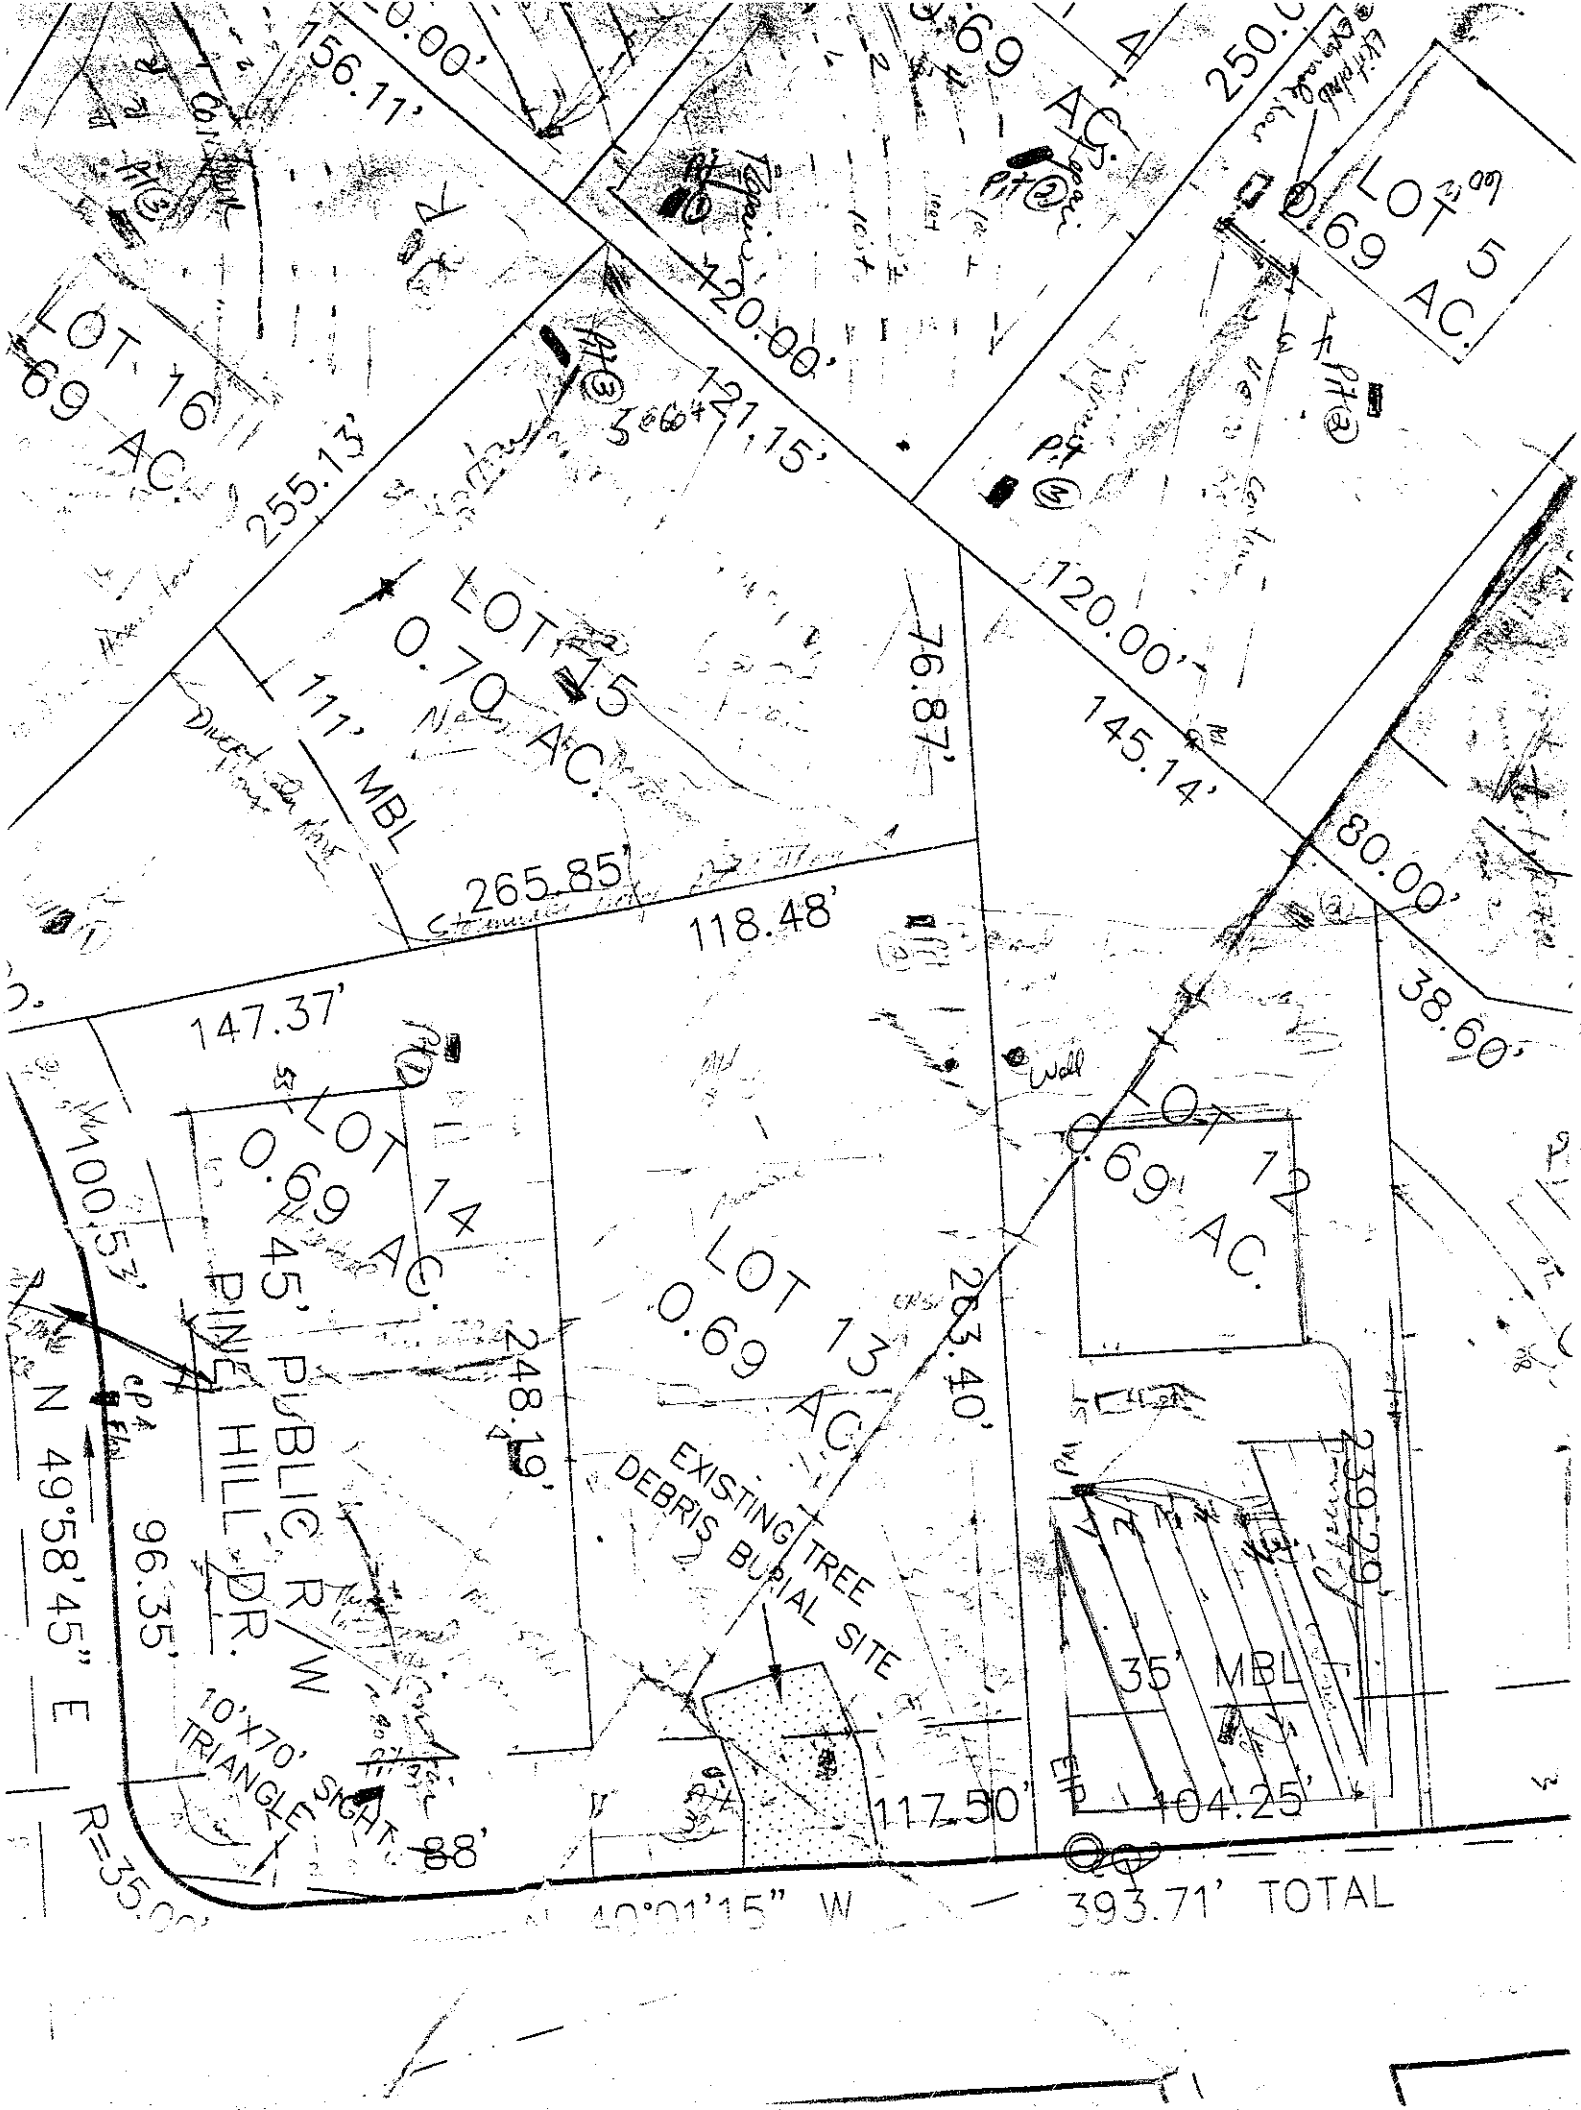
SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

OWNER: MJ Fox APPLICANT: _____
ADDRESS: _____ APPLICATION DATE: _____ DATE EVALUATED: 1-21-99
PROPOSED FACILITY: _____ PROPOSED DESIGN FLOW (.1949): _____ PROPERTY SIZE: _____
LOCATION OF SITE: Lot 12 Lakeview Heights PROPERTY RECORDED: _____
WATER SUPPLY: ☐ Private ☐ Public ☐ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☐ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☐ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	.1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LTAR
1		0-4	gr sl sb hor sl L fr						PS .3
		4-26	SBK co	fr SS SP SE vp					
		26-52	MM SBK pr cl	fr SS SP SE vp					
			few lin SAP	gy mottles					
2		0-8	gr sl sb hor	sl/pl fr SS SP SE vp					PS .3
		8-20	SBK co	fr SS SP SE vp					
		20-47	MASS R, Y, R Cl	fr SS SP SE vp					
			few lin SAP near pit bottom						
3		0-20	SBK, RC/cl	fr SS SP SE vp					PS .3
		20-48	MASS/lin pr cl	few lin SAP fr SS SP SE vp					
4	11/3/05	0-20	R C/cl m SBK	SS, SP, SE, FR					PS.
		20-48	R/R-R	cl-w/SBK SS, SP, SE, FR w/few to many					
			SAP	Inclus of Common Mica Flakes					.3

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)		
System Type(s)		
Site LTAR		

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): _____
EVALUATED BY: _____
OTHER(S) PRESENT: _____


LOT 16
0.69 AC.
LOT 15
0.70 AC.
LOT 14
0.69 AC.
LOT 13
0.69 AC.
LOT 12
0.69 AC.
LOT 5
0.69 AC.
156.11'
420.00'
121.15'
255.13'
120.00'
145.14'
80.00'
38.60'
76.87'
111' MBL
265.85'
118.48'
147.37'
100.53'
248.19'
263.40'
239.29'
35' MBL
104.25'
117.50'
96.35'
88'
393.71' TOTAL
PINE HILL DR.
PUBLIC R/W
45'
EXISTING TREE
DEBRIS BURIAL SITE
10'X70' TRIANGLE
SIGN
Wall
N 49°58'45" E
S 40°01'15" W
R=350.00'
