Sheet ___ of ___
PROPERTY ID #: _____
COUNTY: _____

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

OWNER: _____ APPLICATION DATE _____
ADDRESS: _____ DATE EVALUATED: _____
PROPOSED FACILITY: _____ PROPOSED DESIGN FLOW (.1949): _____ PROPERTY SIZE: _____
LOCATION OF SITE: lot 12 Sundown PROPERTY RECORDED: _____
WATER SUPPLY: ☐ Private ☐ Public ☐ Well ☐ Spring ☐ Other _____
EVALUATION METHOD: ☐ Auger Boring ☐ Pit ☐ Cut
TYPE OF WASTEWATER: ☐ Sewage ☐ Industrial Process ☐ Mixed

PROFILE #	.1940 LAND-SCAPE POSITION/ SLOPE %	HORI-ZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LTAR
1		0-20	RL mk	fi SP					.75
		20-30	RLL msm	fi SBK SP					.3
		30-50	LSAP	fi SBK SP + CL Inc					
2		0-24	SC WSBK	fi SP	common many	many			.75
		24-48	SCL WSBK	fi SP +					.2 - .25
3		0-8	SL						LPP .1
		8-33	C SBK	SP +	common many/SAT Hyd SAP Mang Concretions				
		33-48	SCL Mottled						
4		0-22	YR SCL	WSBK fi SBK SP					(4)
		22-42	YB Mottled						
		42+	Gravelly Soil						

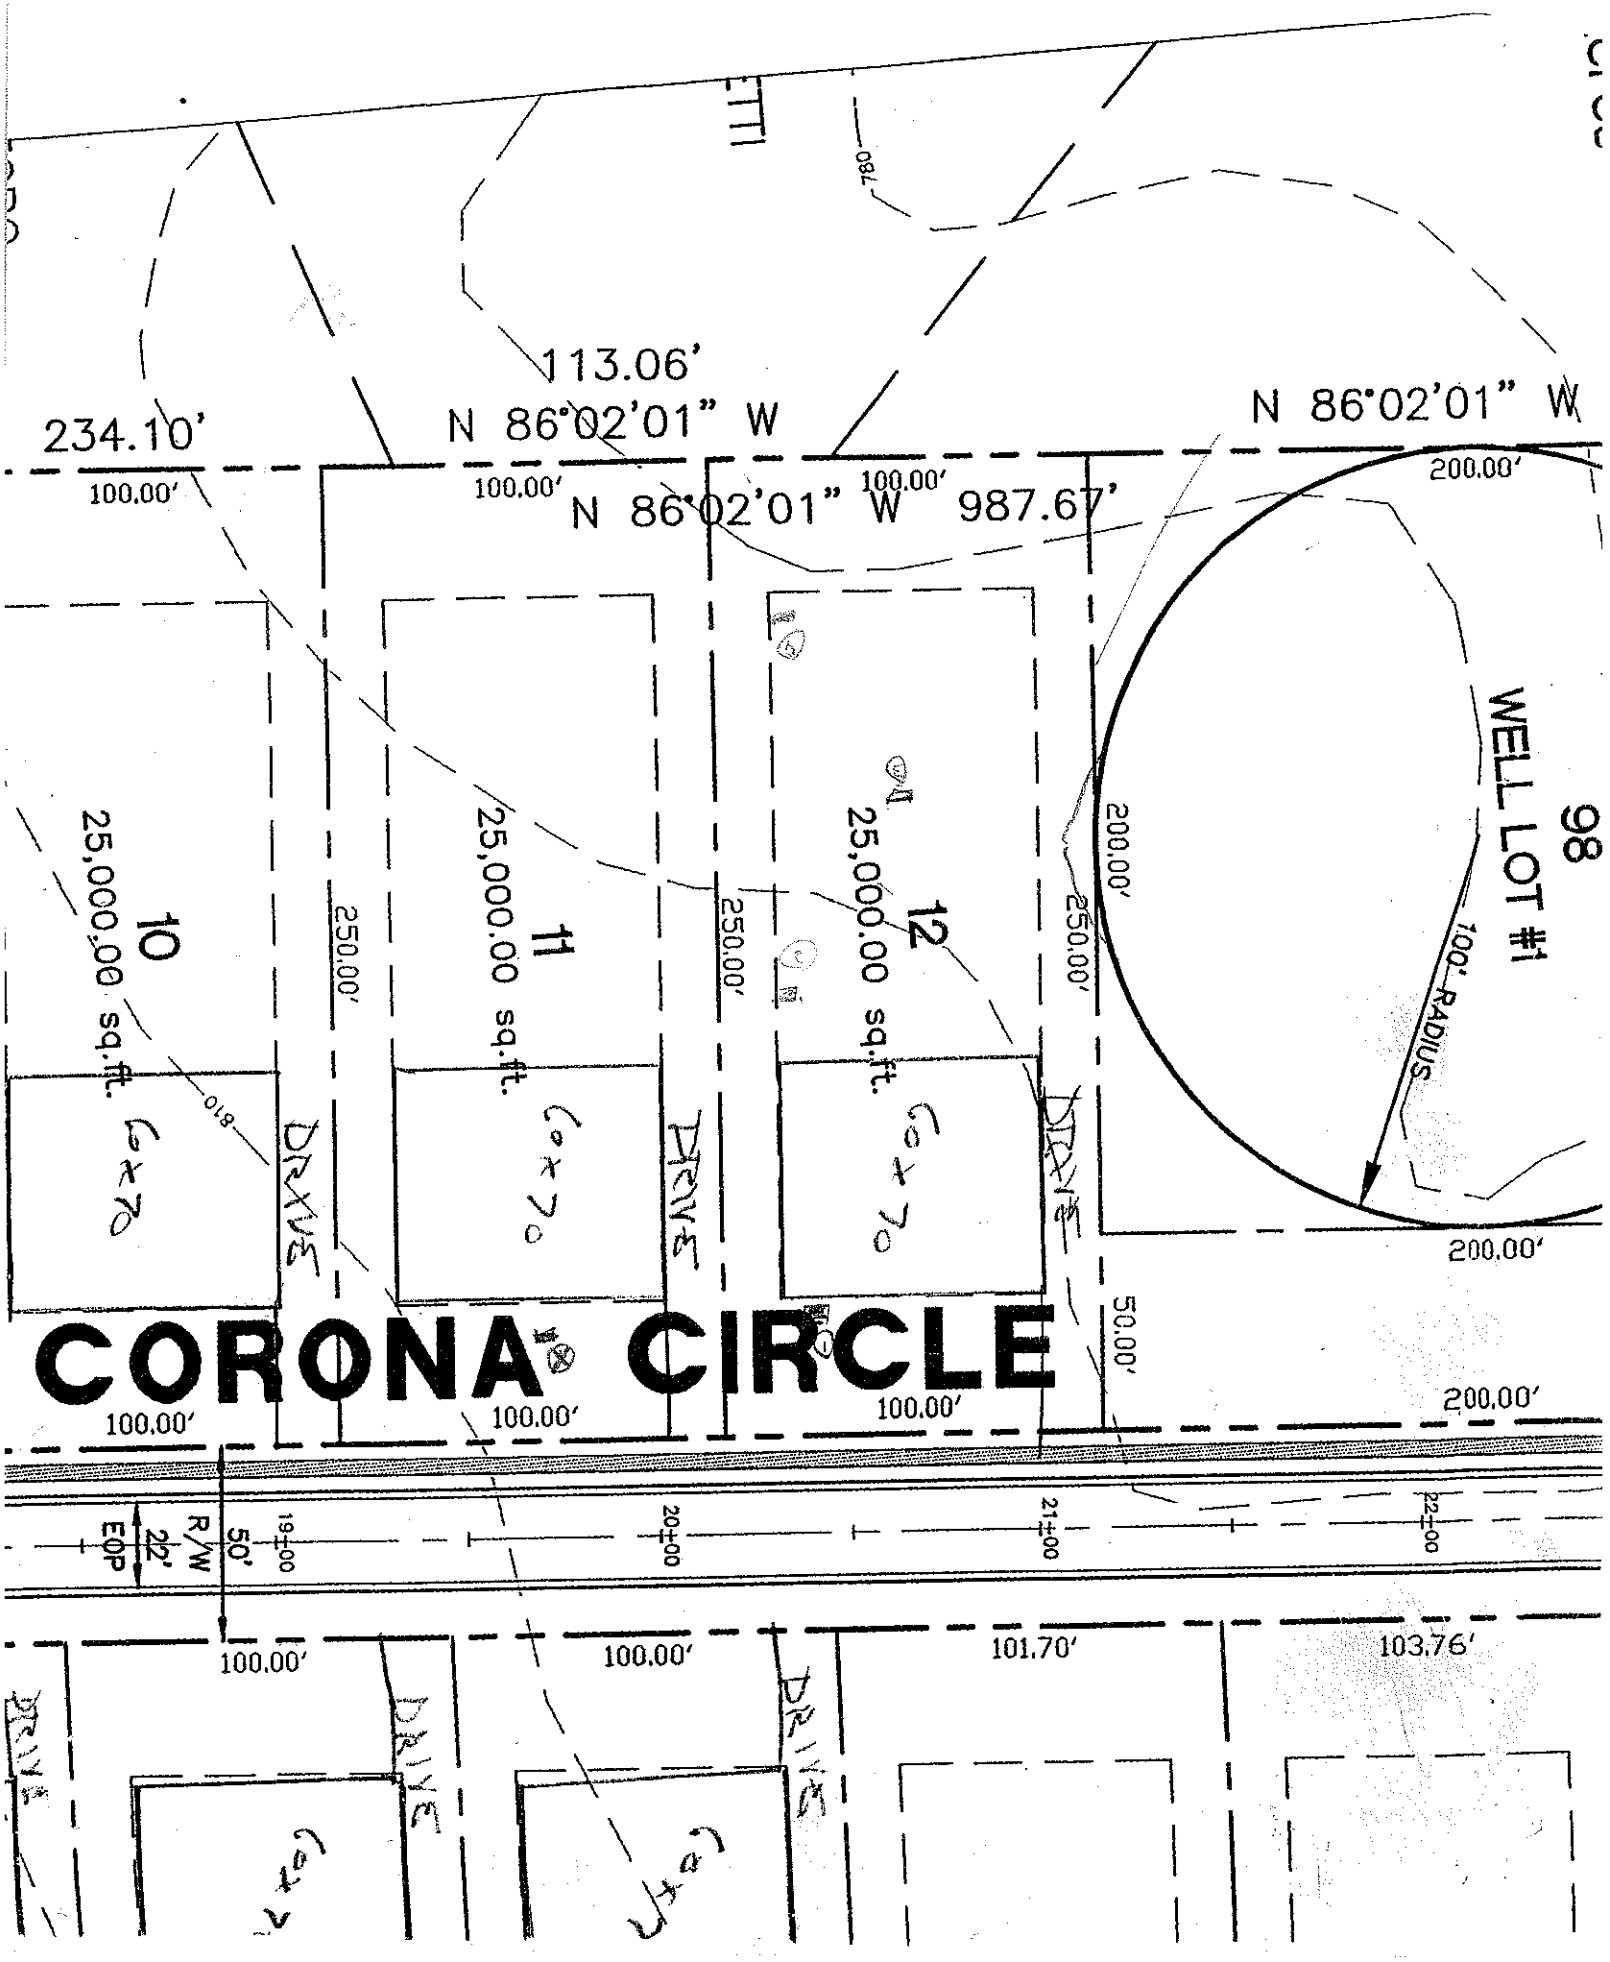
DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)		
System Type(s)		
Site LTAR		

OTHER FACTORS (.1946): _____
SITE CLASSIFICATION (.1948): _____
EVALUATED BY: _____
OTHER(S) PRESENT: _____

COMMENTS: _____

Front of lot 11
0-48 LC SBK fi SP
.3

1" = 100'
60' R/W
N 87°29'04" W
300.20'
140
274.60'
134.60
120'±
130'
REMOTE SEPTIC AREA
158'±
516.44'
216.39'
146.39'
388.49'
138.00'
N 31°15'09"
240.21'
85.49'
82.00'
N 46°01'00" W
260.57'
N 66°07'
6
5
4BR LP
25%


113.06'
N 86°02'01" W
234.10'
100.00'
100.00'
N 86°02'01" W 987.67'
N 86°02'01" W
200.00'
WELL LOT #1
98
100' RADIUS
200.00'
200.00'
10
25,000.00 sq.ft.
11
25,000.00 sq.ft.
12
25,000.00 sq.ft.
250.00'
250.00'
250.00'
50.00'
DRIVE
DRIVE
DRIVE
CORONA CIRCLE
100.00'
100.00'
100.00'
200.00'
R/W 50'
EOP 22'
19+00
20+00
21+00
22+00
100.00'
100.00'
101.70'
103.76'
DRIVE
DRIVE
DRIVE
