DENR/DEH

ON-SITE WASTEWATER SECTION

Sheet 1 of 1
PROPERTY ID #: 47032172122
COUNTY: Iredell

SOIL/SITE EVALUATION
for ON-SITE WASTEWATER SYSTEM

OWNER: April Church
ADDRESS: 203 Star Ln.
PROPOSED FACILITY: SFD
PROPOSED DESIGN FLOW (.1949): 360 gpd
LOCATION OF SITE: 198 Star Ln
APPLICATION DATE: 10-8-14
DATE EVALUATED: 10-27-14
PROPERTY SIZE: 2.56 acres
PROPERTY RECORDED: Yes
WATER SUPPLY: • (Private) • Public • Well • Spring • Other N/A
EVALUATION METHOD: • (Auger Boring) • Pit • Cut
TYPE OF WASTEWATER: • (Sewage) • Industrial Process • Mixed

PROFILE #	.1940 LANDSCAPE POSITION/ SLOPE %	HORIZON DEPTH (IN.)	SOIL MORPHOLOGY (.1941) .1941 STRUCTURE/ TEXTURE	.1941 CONSISTENCE/ MINERALOGY	OTHER PROFILE FACTORS .1942 SOIL WETNESS/ COLOR	.1943 SOIL DEPTH	.1956 SAPRO CLASS	.1944 RESTR HORIZ	PROFILE CLASS & LTAR
1	16% slight HS	0-10	SL sbk	Fr ssp mod SE	>48"	>48"	>48"	>48"	PS 0.25
		10-26	C sbk	fi slp mod SE					
		26-48	Cl mag deposits wsbk	Fr Mod SE					
2	6% slight HS	0-10	SC sbk	Fr Mod SE	>48"	>48"	>48"	>48"	PS 0.25
		10-28	C sbk	Fi slp mod SE					
		28-48	Cl mag deposits wsbk	Fr Mod SE					
3	5% slight HS	0-5	SC sbk	Fr Mod SE	>48"	>48"	>48"	>48"	PS 0.25
		5-33	C sbk	Fi slp mod SE					
		33-48	Cl mag deposits wsbk	Fr Mod SE					
4	6% slight HS	0-6	SC sbk	Fr Mod SE	>48"	>48"	>48"	>48"	PS 0.25
		6-32	C sbk	Fi slp mod SE					
		32-48	Cl mag deposits wsbk	Fr Mod SE					

DESCRIPTION	INITIAL SYSTEM	REPAIR SYSTEM
Available Space (.1945)	PS	PS
System Type(s)	III	III
Site LTAR	0.25	0.25

OTHER FACTORS (.1946): N/A
SITE CLASSIFICATION (.1948): PS
EVALUATED BY: Justin Rhodes
OTHER(S) PRESENT: N/A

COMMENTS: N/A

LEGEND

use the following standard abbreviations

LANDSCAPE POSITION	GROUP	SOIL TEXTURE	CONVENTIONAL .1955 LTAR*	LPP .1957 LTAR*	MINERALOGY/ CONSISTENCE	STRUCTURE
CC (Concave Slope)	I	S (Sand)	1.2 - 0.8	0.6 - 0.4	NEXP (Non-expansive)	G (Single Grain)
CV (Convex Slope)		LS (Loamy Sand)			SEXP (Slightly Expansive)	M (Massive)
D (Drainage Way)					EXP (Expansive)	CR (Crumb)
DS (Debris Slump)	II	SL (Sandy Loam)	0.8 - 0.6	0.4 - 0.3		GR (Granular)
FP (Flood Plain)		L (Loam)				SBK (Subangular Blocky)
FS (Foot Slope)						ABK (Angular Blocky)
H (Head Slope)	III	Si (Silt)	0.6 - 0.3	0.3 - 0.15		PL (Platy)
L (Linear Slope)		SiCL (Silty Clay Loam)				PR (Prismatic)
N (Nose Slope)		CL (Clay Loam)				
R (Ridge)		SCL (Sandy Clay Loam)			**MOIST**	**WET**
S (Shoulder Slope)		SiL (Silt Loam)				
T (Terrace)					VFR (Very Friable)	NS (Non-sticky)
	IV	SC (Sandy Clay)	0.4 - 0.1	0.2 - 0.05	FR (Friable)	SS (Slightly Sticky)
		SiC (Silty Clay)			FI (Firm)	S (Sticky)
		C (Clay)			VFI (Very Firm v. Very Sticky)	VS (Very Sticky)
		O (Organic)	None	None	EFI (Extremely Firm)	NP (Non-plastic)
						SP (Slightly Plastic)
						P (Plastic)
						VP (Very Plastic)

*Adjust LTAR due to depth, consistence, structure, soil wetness, landscape, position, wastewater flow and quality.


NOTES

HORIZON DEPTH	In inches below natural soil surface
DEPTH OF FILL	In inches from land surface
RESTRICTIVE HORIZON	Thickness and depth from land surface
SAPROLITE	S(suitable) or U(unsuitable)
SOIL WETNESS	Inches from land surface to free water or inches from land surface to soil colors with chroma 2 or less - record Munsell color chip designation
CLASSIFICATION	S (Suitable), PS (Provisionally Suitable), or U (Unsuitable)


Evaluation of saprolite shall be by pits.

Long-term Acceptance Rate (LTAR): gal/day/ft^2

Show profile locations and other site features (dimensions, reference or benchmark, and North).

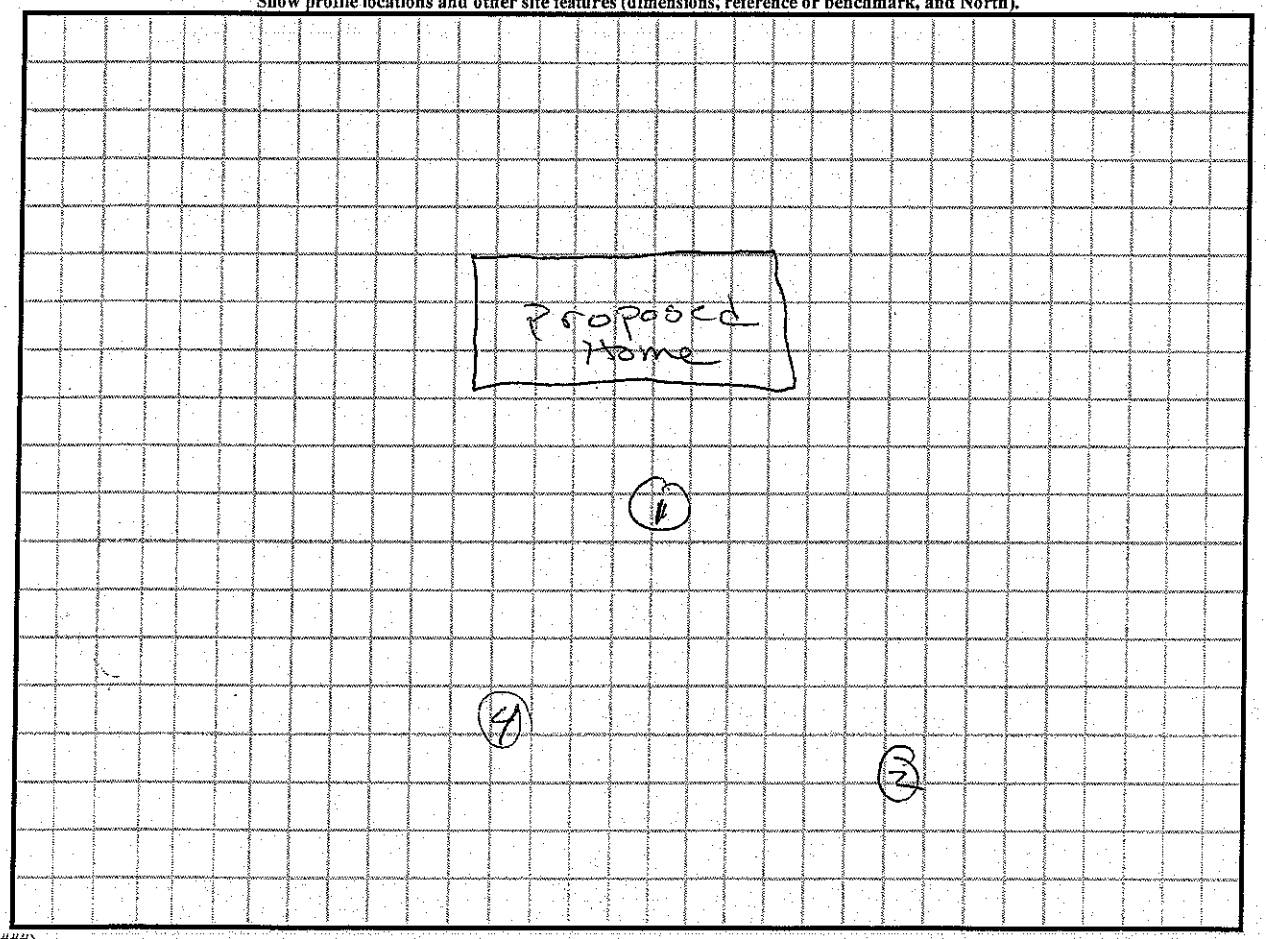

DENR (######)
Review (#####)

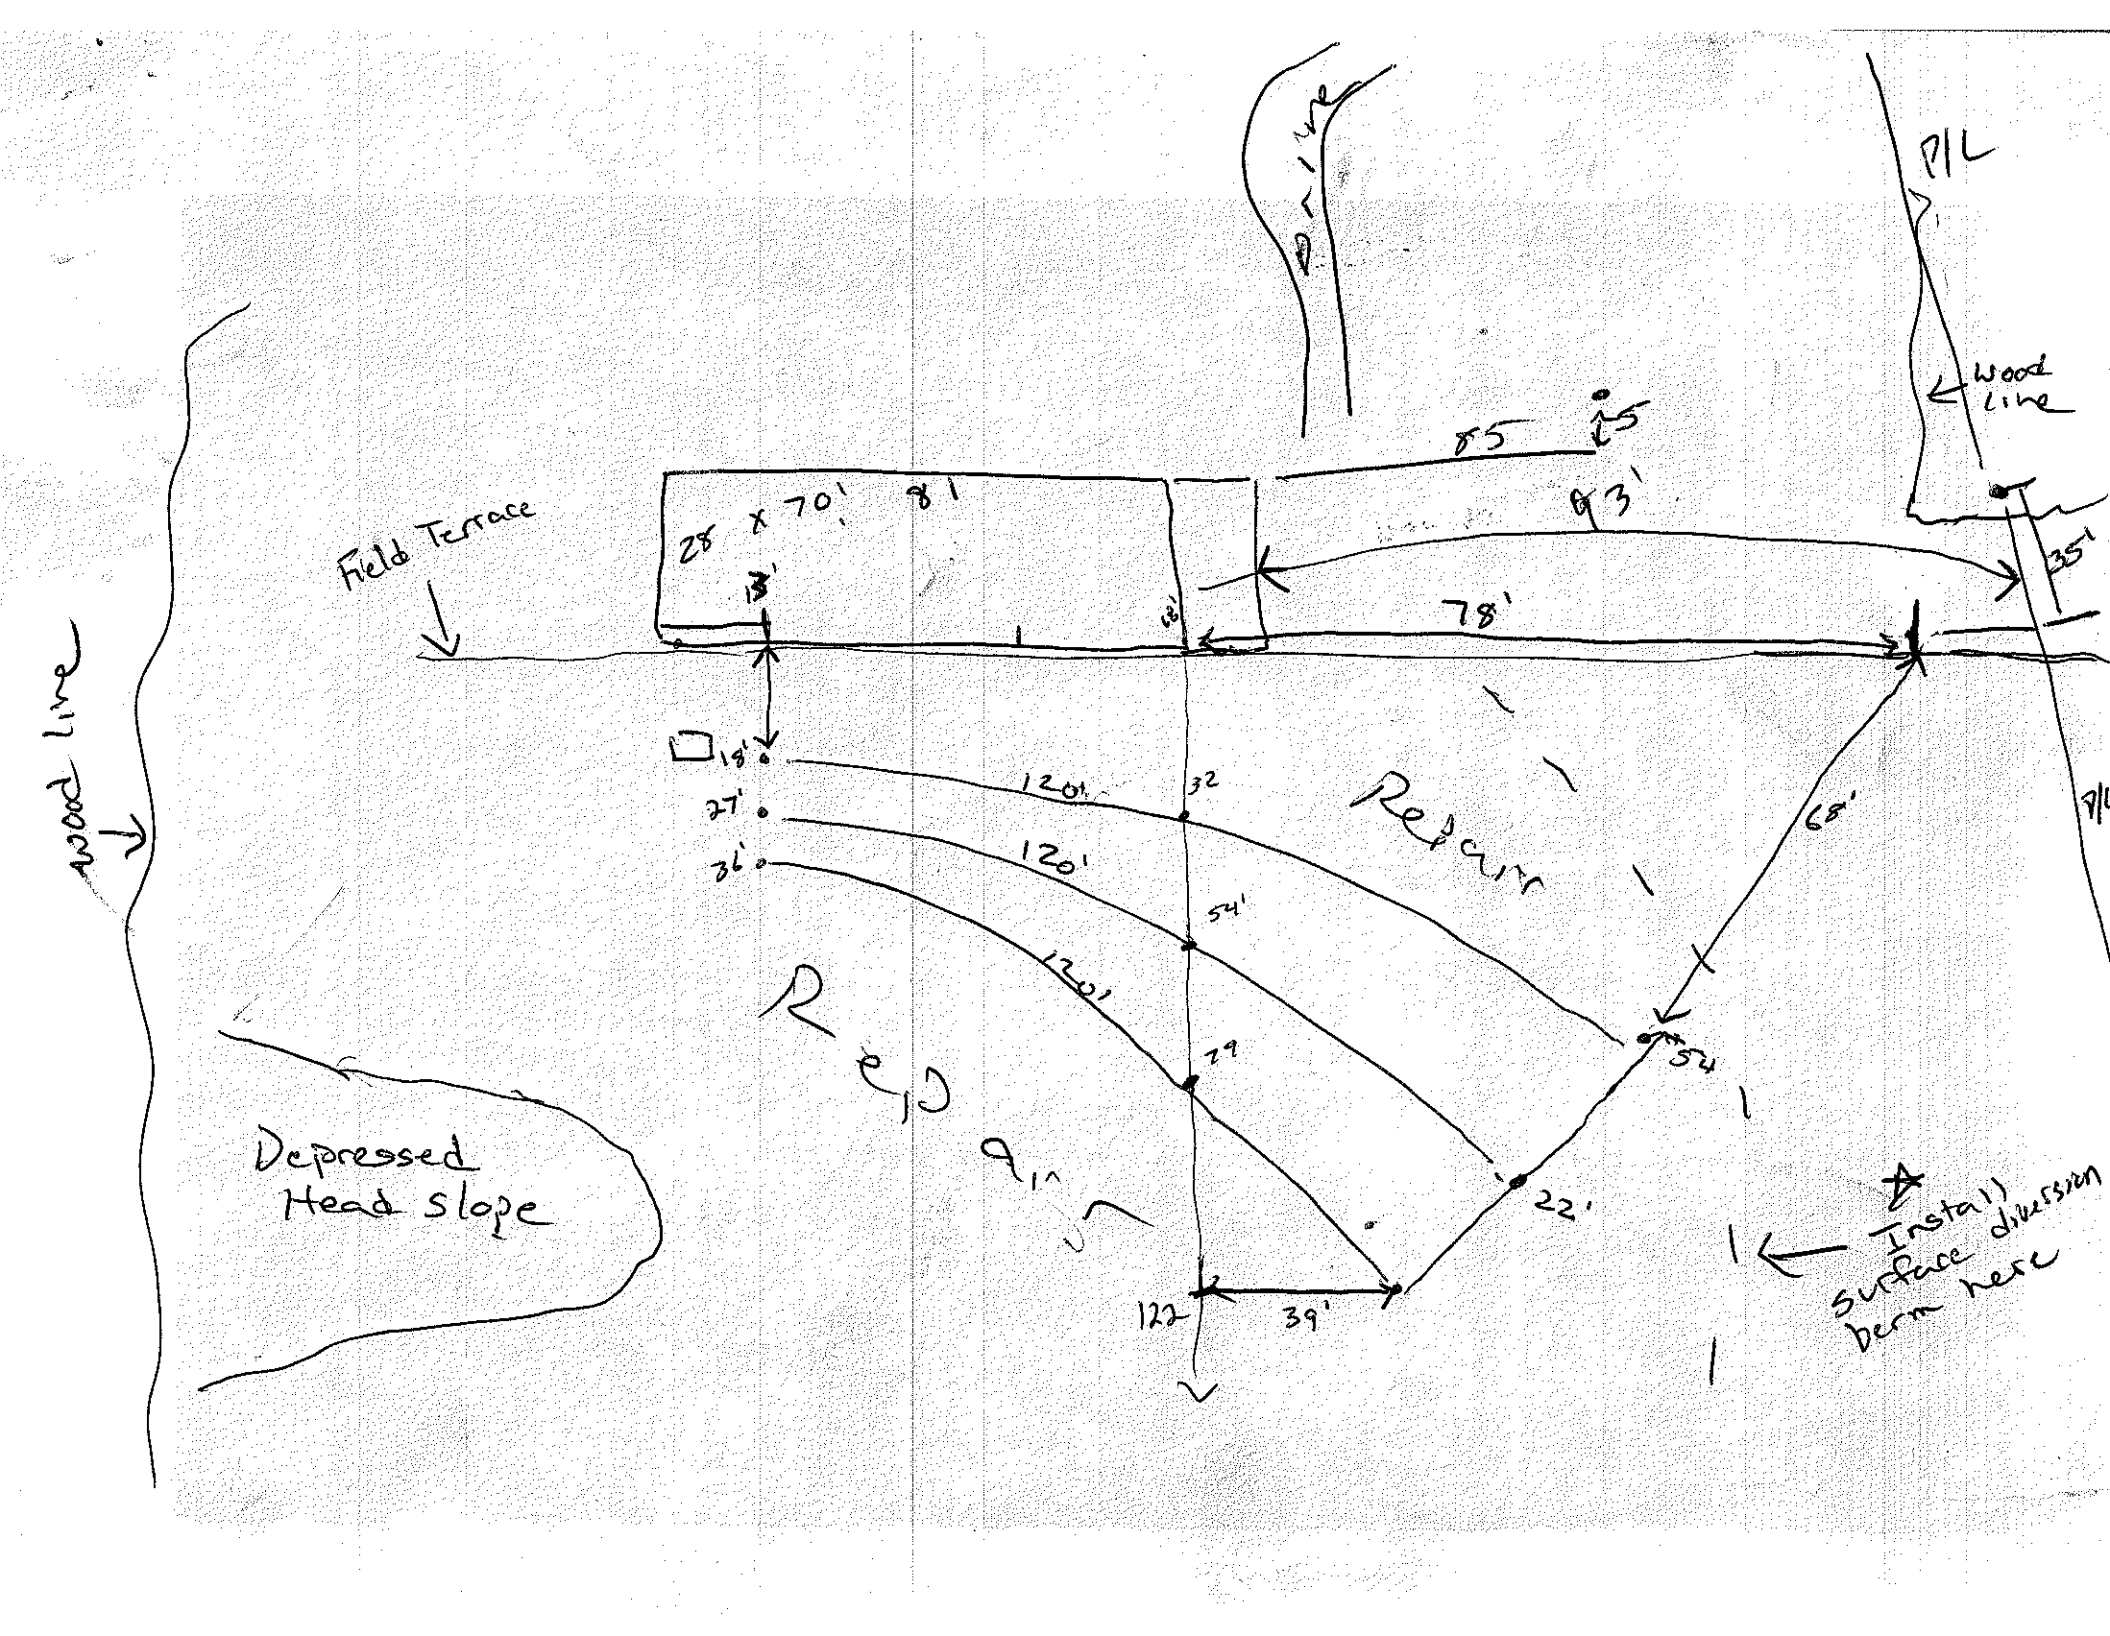
P/L
Wood line
85'
93'
35'
Field Terrace
28 x 70' 81'
13'
63'
78'
18'
27'
36'
120'
120'
120'
32
54'
79
122
39'
22'
54
65'
Return
Return
Wood line
Depressed Head slope
Install surface diversion berm here
P/L
